



CITY OF FORT LAUDERDALE

**MEETING MINUTES
CITY OF FORT LAUDERDALE
FIRE-RESCUE FACILITIES BOND ISSUE
BLUE RIBBON COMMITTEE
FORT LAUDERDALE CITY HALL
100 N. ANDREWS AVENUE
FORT LAUDERDALE, FLORIDA, 33301
VIRTUAL MEETING
THURSDAY, SEPTEMBER 24, 2020
6:00 P.M.**

Committee Members		Attendance – January / December 2020	
		Present	Absent
Douglas Meade, Chair	P	4	1
Frank Snedaker, Vice Chair	P	5	0
Mark Booth	P	4	1
Raymond Dettmann	P	5	0
Patrick Dirindin	P	3	0
Don Larson	P	4	1
Charles Tatelbaum	P	5	0

Staff

Danica Grujicic, Project Manager II
Irina Tokar, Senior Project Manager
Jill Prizlee, Chief Engineer
Betty Crews, Administrative Assistant
Robert Bacic, Deputy Fire Chief
Brigitte Chiapetta, Recording Secretary, Prototype, Inc.

1. Call to Order

The meeting was called to order at 6:01 p.m.

• Roll Call

Roll was called and it was noted a quorum was present.

2. Approval of Previous Meeting Minutes

• August 27, 2020

Motion made by Mr. Snedaker, seconded by Mr. Booth, to approve. In a voice vote, the **motion** passed unanimously.

Staff Liaison Report

- **Project Status – FS 8 and FS 13**

Senior Project Manager Irina Tokar apologized that the packet was not delivered to Patrick; they had the wrong address.

Chair Meade commented that the entire package is not necessary, mostly the plans of the buildings.

Ms. Tokar stated that everything could be sent via email and if anyone wanted a hard copy it could be distributed. Exhibit 1 is the Fire Bond Expenditure Report. Exhibit 2 is a rezone for Fort Lauderdale Fire Rescue. There were no questions on either of the Exhibits.

Fire Station #8:

Ms. Tokar reported that construction is 91% complete and the substantial completion date is projected to be October 14, 2020. She read her Memorandum to the Board dated September 17, 2020. There were no questions.

Fire Station #13:

Ms. Tokar read her Memorandum to the Board dated September 17, 2020.

Mr. Snedaker asked what the qualification criteria for GIP grant is and if we met it. Ms. Tokar advised that the criteria to show the proposed project is strengthening infrastructure. One of the requirements they did not meet, but were advised to submit, was a CDBG objective; however, the project met qualifications for all other requirements. She noted that partially or fully funding the grant depends on how many requests are received. She believes funds distributed are substantial.

Temporary Fire Station #13:

Ms. Tokar read her Memorandum to the Board dated September 17, 2020. There were no questions.

3. Communication to the City Commission

In response to Chair Meade, all members saw the Communication to the City Commission. He questioned the process and if the Commission saw this or if it is presented at their next meeting.

Ms. Tokar stated that meeting minutes must be submitted with discussion on the topic to the City Clerk's office, then they put the item together. The item will be presented next

month; it will be on the October agenda. She will let the Board know when the item will be discussed.

Chair Meade commented that if anyone wants to take an initiative to send something similar to their individual Commissioners it would probably help the situation.

Mr. Tatelbaum advised that he already sent it to Commissioner Sorenson, and he committed to do whatever he could to assist.

Motion made by Mr. Booth, seconded by Mr. Snedaker, to authorize the Chair to submit a letter to the City Commission on behalf of the committee. In a voice vote, the **motion** passed unanimously.

4. Proposed Visit to FS 8 by Committee Members upon Completion of Project

Chair Meade questioned when the Board would be visiting Fire Station #8.

Ms. Tokar advised once they have a date for substantial completion, if the Committee would like, they would be happy to arrange a visit to the site.

There was a consensus to visit the site. Chair Meade questioned if the visit would be at the end of October.

Ms. Tokar stated replied yes and stated that Ms. Crews would coordinate with everyone to find a time.

In response to Chair Meade, Deputy Fire Chief Basic stated meetings cannot be held at that location as there is no community room.

5. Adjournment – Next regular meeting: October 22, 2020

There being no further business to come before the Committee at this time, the meeting was adjourned at 6:14 p.m.

Any written public comments made 48 hours prior to the meeting regarding items discussed during the proceedings have been attached hereto.

[Minutes prepared by C.Guifarro, Prototype, Inc.]



Memorandum

To: Fire-Rescue Bond Committee
From: Irina Tokar, RA, Senior Project Manager
Date: September 17, 2020
Re: Fire-Rescue Facilities Bond Issue Blue Ribbon Committee Update

The purpose of this Memorandum is to provide an update on the two (2) remaining fire station projects and one (1) temporary fire station.

Please see the current fire bond expenditures report (Exhibit I). Please refer to Exhibit II for proposed rezone for Fort Lauderdale Fire Rescue.

Fire Station #8

The construction is 91% complete based on the current billing. The substantial completion date is projected to be on 10/14/2020 (Exhibit III). The work associated with the traffic signalization will be done at later date once we finalize the agreement with Florida East Coast Railway (FEC). The work progresses on schedule. Currently the contractor is working on cabinets installation, irrigation, gym flooring, security systems, and generator start-up. Contractor completed fencing and epoxy flooring. Please see Exhibit IV for progress pictures of the site.

We are working with Florida East Coast Railway (FEC) on agreement to connect our new crossing warning system to their controller to allow for signal synchronization. City Attorney Office is reviewing the Agreement with FEC. FEC fees are \$98,330. As part of the emergency vehicle signalization scope, we also need to install approximately 508 linear feet of new 2" conduit including under railroad tracks. The proposed cost from the contractor is \$34,711. FEC stated we will be able to perform the installation under our existing permit.

Fire Station #13

ACAI Associates, Inc., our architectural consultant, is presently working on the schematic design. The consultant completed the site survey and geotechnical testing. All work is progressing as planned and on schedule (Exhibit V). Staff submitted a grant application for Rebuild Florida General Infrastructure Program (GIP) in the amount of \$4,100,000 to request additional construction funding. Currently Florida Department of Economic Opportunity (DEO) is conducting applications scoring.

We anticipate starting the construction in May of 2022.





Temporary Fire Station #13

Craven Thompson & Associates (CTA) continues the design development. The project is on schedule (Exhibit VI). CTA and City Staff presented the project to Planning and Zoning Board (PZB) for approval of a Land Use Amendment to allow the temporary fire station on the property. The PZB voted to approve the amendment on September 16, 2020 and the project will be presented to City Commission for the final approval of Site Plan Level IV. The approval will require two readings at Commission and is expected to be completed at the second meeting in November 2020.

The current projected date to start construction is April 2021.

Attachments:

- Exhibit I: Fire Rescue Bond Expenditures
- Exhibit II: Proposed Rezone Fire Rescue Map
- Exhibit III: Construction Schedule Fire Station #8
- Exhibit IV: Progress Pictures Fire Station #8
- Exhibit V: Design Schedule #13
- Exhibit VI: Design Schedule Temporary Fire Station #13

C: Chris Lagerbloom, City Manager
John Herbst, City Auditor
Laura Reece, Director Office of Management and Budget
Rhoda Mae Kerr, Fire Chief
Robert Basic, Deputy Fire Chief
Raj Verma, Public Works Director
Jill Prizlee, Chief Engineer





CITY OF
FORT LAUDERDALE



EXHIBIT I: Fire Rescue Bond Expenditures

**FIRE RESCUE BOND SERIES 2005 AND 2011
AS OF SEPTEMBER 11, 2020**

Project Number	Project Title	Bond Estimate (Exhibit A)	Appropriations to Date*	Expenditures to date	Unspent Balance	Encumbrance	Funds Available
FIRE RESCUE BOND 2005 SERIES FUND (336)							
COMPLETED STATIONS							
P10363	**EXEC AIRPORT ARFF/EOC BUILDING	3,535,000	6,050,721	6,050,721	-	-	-
P10766	REPLACEMENT FIRE STATION 47	3,760,000	4,033,510	4,033,510	-	-	-
P10905	FIRE STATION 29 DESIGN & CONSTRUCTION	3,760,000	3,847,235	3,847,235	-	-	-
P10910	FIRE STATION SOUTHEAST LAND ACQUISITION	1,350,000	9,500	9,500	-	-	-
P10911	FIRE STATION 46 DESIGN & CONSTRUCTION	3,760,000	3,356,804	3,356,804	-	-	-
P10912	FIRE STATION 49 DESIGN & CONSTRUCTION	-	3,860,394	3,860,394	-	-	-
P10914	NEW FIRE STATION 54	3,760,000	5,118,873	5,007,088	111,786	100,080	11,706
P10916	NEW FIRE STATION 3	3,760,000	2,777,833	2,777,833	-	-	-
P10919	NEW FIRE STATION 35	4,510,000	3,627,073	3,627,073	-	-	-
P11238	TEMPORARY FIRE STATION 29 MODIFICATIONS	-	119,394	119,394	-	-	-
P11368	TEMPORARY FIRE STATION 49	3,760,000	309,655	309,655	-	-	-
P11892	TEMPORARY FIRE STATION 54	-	420,748	420,748	-	-	-
COMPLETED STATIONS TOTAL		31,955,000	33,531,740	33,419,955	111,786	100,080	11,706
NON-STATION RELATED COSTS							
P00274	BOND AND OTHER FINANCIAL EXPENSES	-	706,838	706,838	-	-	-
P11024	NEW FIRE STATIONS SHARED PROJECT COSTS	-	23,105	23,105	-	-	-
P11576	FIRE STATION FEASIBILITY STUDY	-	68,000	68,000	-	-	-
NON-STATION RELATED COSTS TOTAL		-	797,943	797,943	-	-	-
STATIONS TO BE COMPLETED							
P10909	NEW SOUTHEAST FIRE STATION 8	3,535,000	5,197,260	4,551,418	645,841	645,766	75
P10918	NEW FIRE STATION 13	4,510,000	4,671,646	171,040	4,500,606	671,097	3,829,509
STATIONS TO BE COMPLETED TOTAL		8,045,000	9,868,906	4,722,458	5,146,447	1,316,863	3,829,584
FIRE RESCUE BOND 2005 SERIES FUND (336) TOTAL		40,000,000	44,198,589	38,940,356	5,258,233	1,416,943	3,841,290
GENERAL CAPITAL PROJECTS FUND (331)							
COMPLETED STATIONS							
P10363	**EXEC AIRPORT ARFF/EOC BUILDING	N/A	593,711	593,711	-	-	-
P10766	REPLACEMENT FIRE STATION 47	N/A	1,019,348	1,019,348	-	-	-
P10914	NEW FIRE STATION 54	N/A	316,674	316,673	1	-	1
P10916	NEW FIRE STATION 3	N/A	71,846	71,846	-	-	-
COMPLETED STATIONS TOTAL			2,001,579	2,001,578	1	-	1

**FIRE RESCUE BOND SERIES 2005 AND 2011
AS OF SEPTEMBER 11, 2020**

Project Number	Project Title	Bond Estimate (Exhibit A)	Appropriations to Date*	Expenditures to date	Unspent Balance	Encumbrance	Funds Available
STATIONS TO BE COMPLETED							
P10909	NEW SOUTHEAST FIRE STATION 8	N/A	644,256	493,050	151,206	151,206	-
P10918	NEW FIRE STATION 13	N/A	106,000	27,633	78,347	-	78,347
P12509	TEMPORARY FIRE STATION 13		380,000	114,335	265,665	81,453	184,212
STATIONS TO BE COMPLETED TOTAL			1,130,256	635,018	495,218	232,659	262,559
GENERAL CAPITAL PROJECTS FUND (331) TOTAL			3,131,835	2,636,596	495,219	232,659	262,560
PARKING FUND (461)							
COMPLETED STATIONS							
P10914	NEW FIRE STATION 54	N/A	500,000	500,000			
COMPLETED STATIONS TOTAL			500,000	500,000	0	0	0
STATIONS TO BE COMPLETED							
P10909	SE FIRE STATION DESIGN & CONSTRUCTION	N/A	50,000	50,000	-	-	-
STATIONS TO BE COMPLETED TOTAL			50,000	50,000	0	-	0
PARKING FUND (461) TOTAL			50,000	50,000	0	-	0
AIRPORT FUND (468)							
COMPLETED STATIONS							
P10363	**EXEC AIRPORT ARFF/EOC BUILDING	N/A	3,593,447	3,593,447	-	-	-
COMPLETED STATIONS TOTAL			3,593,447	3,593,447	-	-	-
AIRPORT FUND (468) TOTAL			3,593,447	3,593,447	-	-	-

* Since 2005, the bond proceeds have earned \$2.5 Million in interest revenue. With the 2011 bond issue, the City received \$400,000 in premiums revenue.

** P10363 Executive Airport ARFF/EOC Building project included airport funds which have been completely spent.



CITY OF
FORT LAUDERDALE



EXHIBIT II: Fort Lauderdale Fire Rescue Map



PROPOSED REZONE 1/27/2020 FORT LAUDERDALE FIRE RESCUE

GIS

2/12/2020

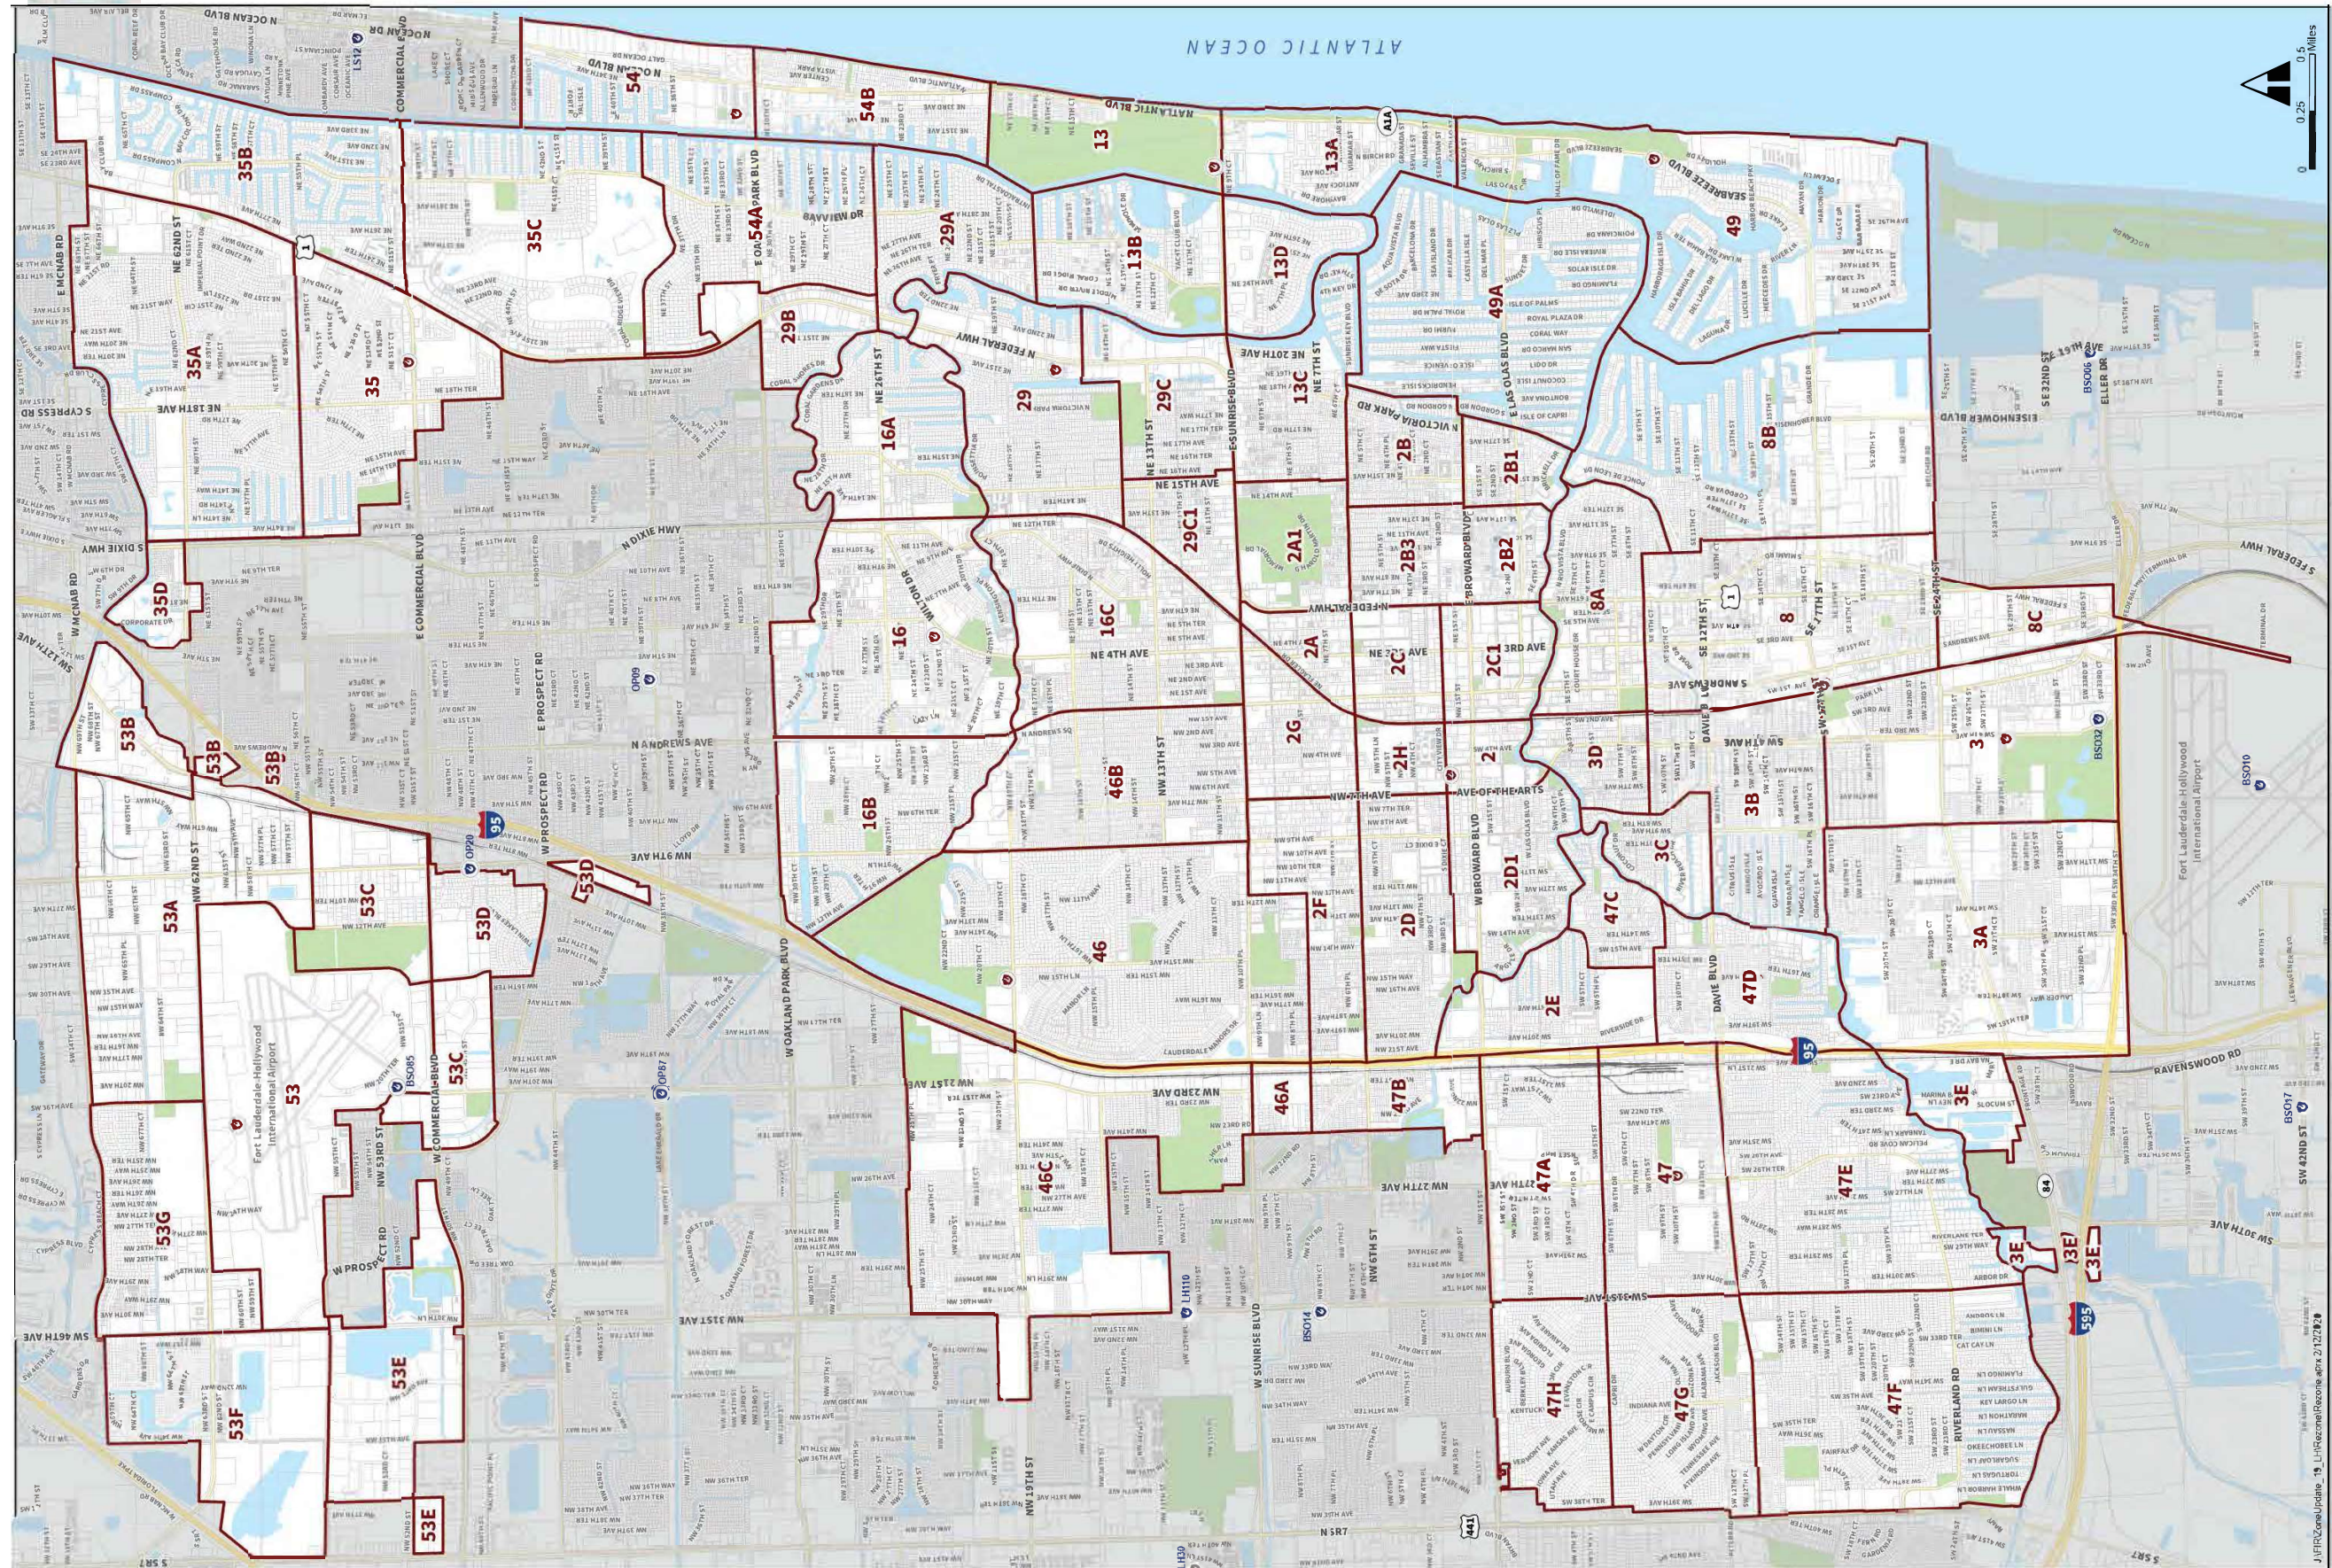


EXHIBIT II

J:\FRZ\Rezone\Rezone_18_1_Hazmat\Rezone_18_1_Hazmat.aprx 2/12/2020



CITY OF
FORT LAUDERDALE



EXHIBIT III: Construction Schedule Fire Station #8, at 1717 SW 1st Avenue

FS8-14R1 - Fire Station 8 - Update 2020-0904R1						FTL Fire Sta - Schedule Update - Data Date = 09/04/20																09/15/20 09:36																													
Activity ID		Activity Name				Orig Dur	Rem Dur	Per Cent Comp	Start	Finish	Qtr 4, 2018			Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019			Qtr 1, 2020			Qtr 2, 2020			Qtr 3, 2020			Qtr 4, 2020			Qtr 1, 2021			Qtr 2, 2021			Qtr 3, 2021			Qtr 4, 2021			22	
											Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	Jan	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	an	
📁 Fire Station 8 - Update 2020-0904R1																																																			
📁 MILESTONE EVENTS																																																			
📁 CONTRACT COMPLETION DATES																																																			
📁 99900		ORIGINAL CONTRACT SUBSTATIAL COMPLETION (360 DAYS)				0	0	100%		10/10/19 A																																◆ ORIGINAL CONTRACT SUBSTATIAL COMPLETION (360 DAYS),									
📁 100009		CHANGE ORDER #1 TIME EXTENSION (7 DAYS)				7	0	100%	10/11/19 A	10/17/19 A																																■ CHANGE ORDER #1 TIME EXTENSION (7 DAYS)									
📁 100019		CO No. 2 - TIME EXTENSION (62 DAYS)				62	0	100%	10/18/19 A	12/18/19 A																																■ CO No. 2 - TIME EXTENSION (62 DAYS)									
📁 99950		ORIGINAL CONTRACT FINAL COMPLETION (390 DAYS)				0	0	100%		11/09/19 A																																◆ ORIGINAL CONTRACT FINAL COMPLETION (390 DAYS),									
📁 100029		CO No. 3 - TIME EXTENSION (11 DAYS)				11	0	100%	12/19/19 A	12/29/19 A																																■ CO No. 3 - TIME EXTENSION (11 DAYS)									
📁 99961		ADJUSTED CONTRACT SUBSTATIAL COMPLETION (440 DAYS)				0	0	100%		12/29/19 A																																◆ ADJUSTED CONTRACT SUBSTATIAL COMPLETION (440 DAYS),									
📁 99971		ADJUSTED CONTRACT FINAL COMPLETION (470 DAYS)				0	0	100%		01/28/20 A																																◆ ADJUSTED CONTRACT FINAL COMPLETION (470 DAYS),									
📁 COMMENCEMENT																																																			
📁 99000		ISSUE SITE PERMIT				1	0	100%	10/15/18 A	01/09/19 A	■ ISSUE SITE PERMIT																																								
📁 90000		NOTICE TO PROCEED				0	0	100%	10/15/18 A		◆ NOTICE TO PROCEED, 10/15/18 A																																								
📁 90100		ISSUE BUILDING PERMIT				1	0	100%	10/15/18 A	01/09/19 A	■ ISSUE BUILDING PERMIT																																								
📁 FINAL INSPECTIONS																																																			
📁 99150		Final Landscape Inspections				2	2	0%	10/05/20	10/06/20																																Final Landscape Inspections									
📁 99110		TCO Mechanical Inspections				3	3	0%	10/07/20	10/09/20																																TCO Mechanical Inspections									
📁 99130		TCO Electrical Inspections				3	3	0%	10/07/20	10/09/20																																TCO Electrical Inspections									
📁 99120		TCO Fire Preliminary Inspection				3	3	0%	10/07/20	10/09/20																																TCO Fire Preliminary Inspection									
📁 99160		Final Public Works Inspection				2	2	0%	10/07/20	10/08/20																																Final Public Works Inspection									
📁 99140		TCO Fire Inspection				3	3	0%	10/12/20	10/14/20																																TCO Fire Inspection									
📁 99170		TCO Building Inspections				2	2	0%	10/13/20	10/14/20																																TCO Building Inspections									
📁 COMPLETION MILESTONES																																																			
📁 99910		(TCO) SUBSTANTIAL COMPLETION FIRE STATION				0	0	0%		10/14/20*																																◆ (TCO) SUBSTANTIAL COMPLETION FIRE STATION,									
📁 99995		PROJECT CLOSEOUT				21	21	0%	10/15/20	11/12/20																																■ PROJECT CLOSEOUT									
📁 99290		Contractor Punch Out				10	10	0%	10/15/20	10/28/20																																■ Contractor Punch Out									
📁 99292		Owner Punch Out				11	11	0%	10/29/20	11/12/20																																■ Owner Punch Out									
📁 99915		(TCO) SUBSTANTIAL COMPLETION - OFF-SITE CONSTRUCTION				0	0	0%		11/11/20*																																◆ (TCO) SUBSTANTIAL COMPLETION - OFF-SITE CONSTRUCTION,									
📁 99999		FINAL COMPLETION				0	0	0%		11/12/20*																																◆ FINAL COMPLETION,									
📁 DELAYS & IMPACTS																																																			
📁 MASTER PERMIT DELAYS																																																			
📁 90110		Obtain Master Building Permit After NTP				10	0	100%	10/15/18 A	01/09/19 A	■ Obtain Master Building Permit After NTP																																								
📁 90120		Master Building Permit Available				1	0	100%	01/09/19 A	01/09/19 A	Master Building Permit Available																																								
📁 90130		Start Construction				1	0	100%	01/10/19 A	01/10/19 A	Start Construction																																								
📁 UNFORESEEN FORCE MAIN PIPE																																																			
📁 90210		Unforseen Force Main Discovered				1	0	100%	01/21/19 A	01/21/19 A	Unforseen Force Main Discovered																																								
📁 90220		Perform Additional Work to Resolve Conflict				7	0	100%	01/21/19 A	01/28/19 A	■ Perform Additional Work to Resolve Conflict																																								
📁 90230		Resume Site Work & Building Pad Construction				1	0	100%	01/29/19 A	01/29/19 A	Resume Site Work & Building Pad Construction																																								
📁 OVERHEAD DOOR DELAY																																																			
📁 93108		Specified Door Not Level "E" - Door Rejected				1	0	100%	04/18/19 A	04/18/19 A	Specified Door Not Level "E" - Door Rejected																																								
📁 93110		Resolve O/H Door Supplier				20	0	100%	04/19/19 A	02/24/20 A	■ Resolve O/H Door Supplier																																								
📁 93120		Owner Approve Change Order for Level "E" Door Supplier				1	0	100%	02/21/20 A	02/21/20 A	Owner Approve Change Order for Level "E" Door Supplier																																								
📁 93124		Approve Shop Drawings				10	0	100%	02/28/20 A	03/25/20 A	■ Approve Shop Drawings																																								
📁 93130		Release New Doors for Fabrication				1	0	100%	03/26/20 A	03/26/20 A	Release New Doors for Fabrication																																								
📁 93220		Fabricate New Doors				40	0	100%	03/26/20 A	04/29/20 A	■ Fabricate New Doors																																								
📁 93230		Custom Powder Coating for New Doors				10	0	100%	04/29/20 A	05/06/20 A	■ Custom Powder Coating for New Doors																																								

FS8-14R1 - Fire Station 8 - Update 2020-0904R1						FTL Fire Sta - Schedule Update - Data Date = 09/04/20												09/15/20 09:36																												
Activity ID	Activity Name	Orig Dur	Rem Dur	Per Cent Comp	Start	Finish	Qtr 4, 2018			Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019			Qtr 1, 2020			Qtr 2, 2020			Qtr 3, 2020			Qtr 4, 2020			Qtr 1, 2021			Qtr 2, 2021			Qtr 3, 2021			Qtr 4, 2021			22
							Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	Jan	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	
 17457	Masonry Above Low Roof (Parapets)	5	0	100%	06/12/19 A	06/21/19 A																																								
 16432	Set Joists & Decking @ High Roof	4	0	100%	06/19/19 A	08/09/19 A																																								
 16406	Masonry Above High Roof (Parapets)	5	0	100%	07/22/19 A	08/01/19 A																																								
 ROOF																																														
 MAIN BUILDING (LOW ROOF)																																														
 16380	Roofing Trades Prep	5	0	100%	08/12/19 A	10/08/19 A																																								
 16384	Dry-In Roof	3	0	100%	10/07/19 A	10/08/19 A																																								
 16382	Install Built-up Roofing	4	0	100%	10/09/19 A	10/13/19 A																																								
 16378	Lightweight Concrete @ Low Roof	3	0	100%	10/10/19 A	10/12/19 A																																								
 16386	Install Parapet Cap Flashing & Roof Trim	4	0	100%	12/02/19 A	12/06/19 A																																								
 APPARATUS AREA(HIGH ROOF)																																														
 17380	Roofing Trades Prep	5	0	100%	08/12/19 A	10/08/19 A																																								
 17384	Dry-In Roof	3	0	100%	10/07/19 A	10/08/19 A																																								
 17382	Install Built-up Roofing	5	0	100%	10/09/19 A	10/13/19 A																																								
 17378	Lightweight Concrete @ High Roof	3	0	100%	10/10/19 A	10/12/19 A																																								
 17386	Install Parapet Cap Flashing & Roof Trim	4	0	100%	12/04/19 A	12/06/19 A																																								
 BUILDING EXTERIOR																																														
 10216	Install Storefront	5	0	100%	08/01/19 A	08/30/19 A																																								
 10210	Install Stucco	24	0	100%	09/05/19 A	10/09/19 A																																								
 10215	Install Parapet Stucco	5	0	100%	09/18/19 A	09/20/19 A																																								
 10214	Install Exterior Doors	5	0	100%	09/20/19 A	09/20/19 A																																								
 10218	Cure Stucco	16	0	100%	10/16/19 A	11/29/19 A																																								
 10224	Paint Exterior	10	3	70%	12/02/19 A	09/09/20																																								
 10238	Install Downspouts	2	0	100%	12/09/19 A	03/07/20 A																																								
 10234	Install Exterior Railing	5	0	100%	05/15/20 A	05/22/20 A																																								
 10222	Install Roof Ladder	3	0	100%	05/22/20 A	05/22/20 A																																								
 10220	Install Exterior Lighting	5	0	100%	06/18/20 A	06/22/20 A																																								
 10230	Install Metal Screen Wall	6	6	0%	09/04/20	09/14/20																																								
 10236	Install Exterior Signage	8	8	0%	09/15/20	09/24/20																																								
 INTERIOR FRAMING & ROUGH-IN																																														
 MAIN BUILDING R-I																																														
 32414	M - Install Windows	5	0	100%	08/01/19 A	08/09/19 A																																								
 32416	M - Layout & Top Track	3	0	100%	08/01/19 A	08/03/19 A																																								
 32422	M - Plumbing Rough	7	0	100%	09/23/19 A	10/04/19 A																																								
 32418	M - Fire Protection Rough	5	0	100%	09/30/19 A	10/04/19 A																																								

FS8-14R1 - Fire Station 8 - Update 2020-0904R1						FTL Fire Sta - Schedule Update - Data Date = 09/04/20												09/15/20 09:36																													
Activity ID	Activity Name	Orig Dur	Rem Dur	Per Cent Comp	Start	Finish	Qtr 4, 2018			Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019			Qtr 1, 2020			Qtr 2, 2020			Qtr 3, 2020			Qtr 4, 2020			Qtr 1, 2021			Qtr 2, 2021			Qtr 3, 2021			Qtr 4, 2021			22	
							Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	Jan	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D		an
 31422	A - Plumbing Rough	6	0	100%	02/05/20 A	02/11/20 A																		 A - Plumbing Rough																							
 31426	A - HVAC Rough	6	0	100%	02/10/20 A	02/26/20 A																		 A -HVAC Rough																							
 31432	A - Framing Inspection	2	0	100%	02/12/20 A	02/26/20 A																		 A -Framing Inspection																							
 31430	A - MEP Rough Inspections	2	0	100%	02/14/20 A	02/26/20 A																		 A -MEP Rough Inspections																							
 INTERIOR FINISHES																																															
 MAIN BUILDING FINISHES																																															
 42440	M - Hang Drywall	4	0	100%	03/03/20 A	03/15/20 A																		 M - Hang Drywall																							
 42442	M - Finish Drywall	4	0	100%	03/16/20 A	03/30/20 A																		 M - Finish Drywall																							
 42441	M - Screw Inspection	1	0	100%	03/16/20 A	03/16/20 A																		 M - Screw Inspection																							
 42446	M - Prime Paint	3	0	100%	04/13/20 A	04/27/20 A																		 M - Prime Paint																							
 42457	M - Install Kitchen Hood	5	0	100%	04/14/20 A	04/16/20 A																		 M - Install Kitchen Hood																							
 42448	M - Wall Tile	8	0	100%	04/27/20 A	05/19/20 A																		 M - Wall Tile																							
 42460	M - Install Ceiling Grid	6	0	100%	04/28/20 A	05/01/20 A																		 M - Install Ceiling Grid																							
 42462	M - Install Light Fixtures	4	0	100%	05/05/20 A	06/22/20 A																		 M - Install Light Fixtures																							
 42468	M - HVAC Trim Out	4	0	100%	06/15/20 A	06/15/20 A																		 M - HVAC Trim Out																							
 42466	M - Fire Protection Trim Out	3	0	100%	06/22/20 A	06/22/20 A																		 M - Fire Protection Trim Out																							
 42477	M - Install Sports Flooring	3	3	0%	07/10/20 A	09/09/20																		 M - Install Sports Flooring																							
 42444	M - 1st Trim - Doors & Base	3	0	100%	07/23/20 A	07/27/20 A																		 M - 1st Trim - Doors & Base																							
 42464	M - Install Ceiling Tiles	5	0	100%	07/23/20 A	07/27/20 A																		 M - Install Ceiling Tiles																							
 42443	M - Install Epoxy Flooring	10	0	100%	07/27/20 A	08/08/20 A																		 M - Install Epoxy Flooring																							
 42445	M - Cure Epoxy Flooring	7	0	100%	08/08/20 A	08/20/20 A																		 M - Cure Epoxy Flooring																							
 42450	M - Install Cabinets	6	6	0%	09/04/20	09/14/20																		 M - Install Cabinets																							
 42456	M - Install Food Service Cabnets	7	7	0%	09/04/20	09/15/20																		 M - Install Food Service Cabnets																							
 42452	M - Install Tops	6	6	0%	09/09/20	09/16/20																		 M - Install Tops																							
 42454	M - Electrical Trim Out	5	5	0%	09/16/20	09/22/20																		 M - Electrical Trim Out																		</					

FS8-14R1 - Fire Station 8 - Update 2020-0904R1						FTL Fire Sta - Schedule Update - Data Date = 09/04/20																		09/15/20 09:36																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
Activity ID	Activity Name	Orig Dur	Rem Dur	Per Cent Comp	Start	Finish	Qtr 4, 2018			Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019			Qtr 1, 2020			Qtr 2, 2020			Qtr 3, 2020			Qtr 4, 2020			Qtr 1, 2021			Qtr 2, 2021			Qtr 3, 2021			Qtr 4, 2021			22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
							Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	Jan	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D		an																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
	65130	Landscaping	4	4	0%	09/21/20	09/24/20																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							</



CITY OF
FORT LAUDERDALE



EXHIBIT IV: Progress Pictures Fire Station #8, at 1717 SW 1st Avenue



City of Ft. Lauderdale Fire Station #8

Print #200823056
Date: 08/23/20
Lat/Lon: 26.099770 -80.143170
Order No. 07717
Aerial Photography, Inc. 954-568-0484

Photo 1: Aerial Photo 1



City of Ft. Lauderdale Fire Station #8

Print #200823057
Date: 08/23/20
Lat/Lon: 26.099770 -80.143170
Order No. 07717
Aerial Photography, Inc. 954-568-0484

Photo 2: Aerial Photo 2



City of Ft. Lauderdale Fire Station #8

Print #200823058
Date: 08/23/20
Lat/Lon: 26.099770 -80.143170
Order No. 07717
Aerial Photography, Inc. 954-568-0484

Photo 3: Aerial Photo 3



Photo 4: South Elevation



Photo 4: East Elevation



Photo 5: South Elevation



Photo 6: Kitchen/Day Room



Photo 7: Restroom



Photo 8: Alarm/Watch Room



Photo 9: Corridor 3



Photo 10: Corridor 2



Photo 11: Corridor 1



Photo 12: Gym




Photo 13: Gym



CITY OF
FORT LAUDERDALE



EXHIBIT V: Design Schedule Fire Station #13, at 2871 E. Sunrise Boulevard

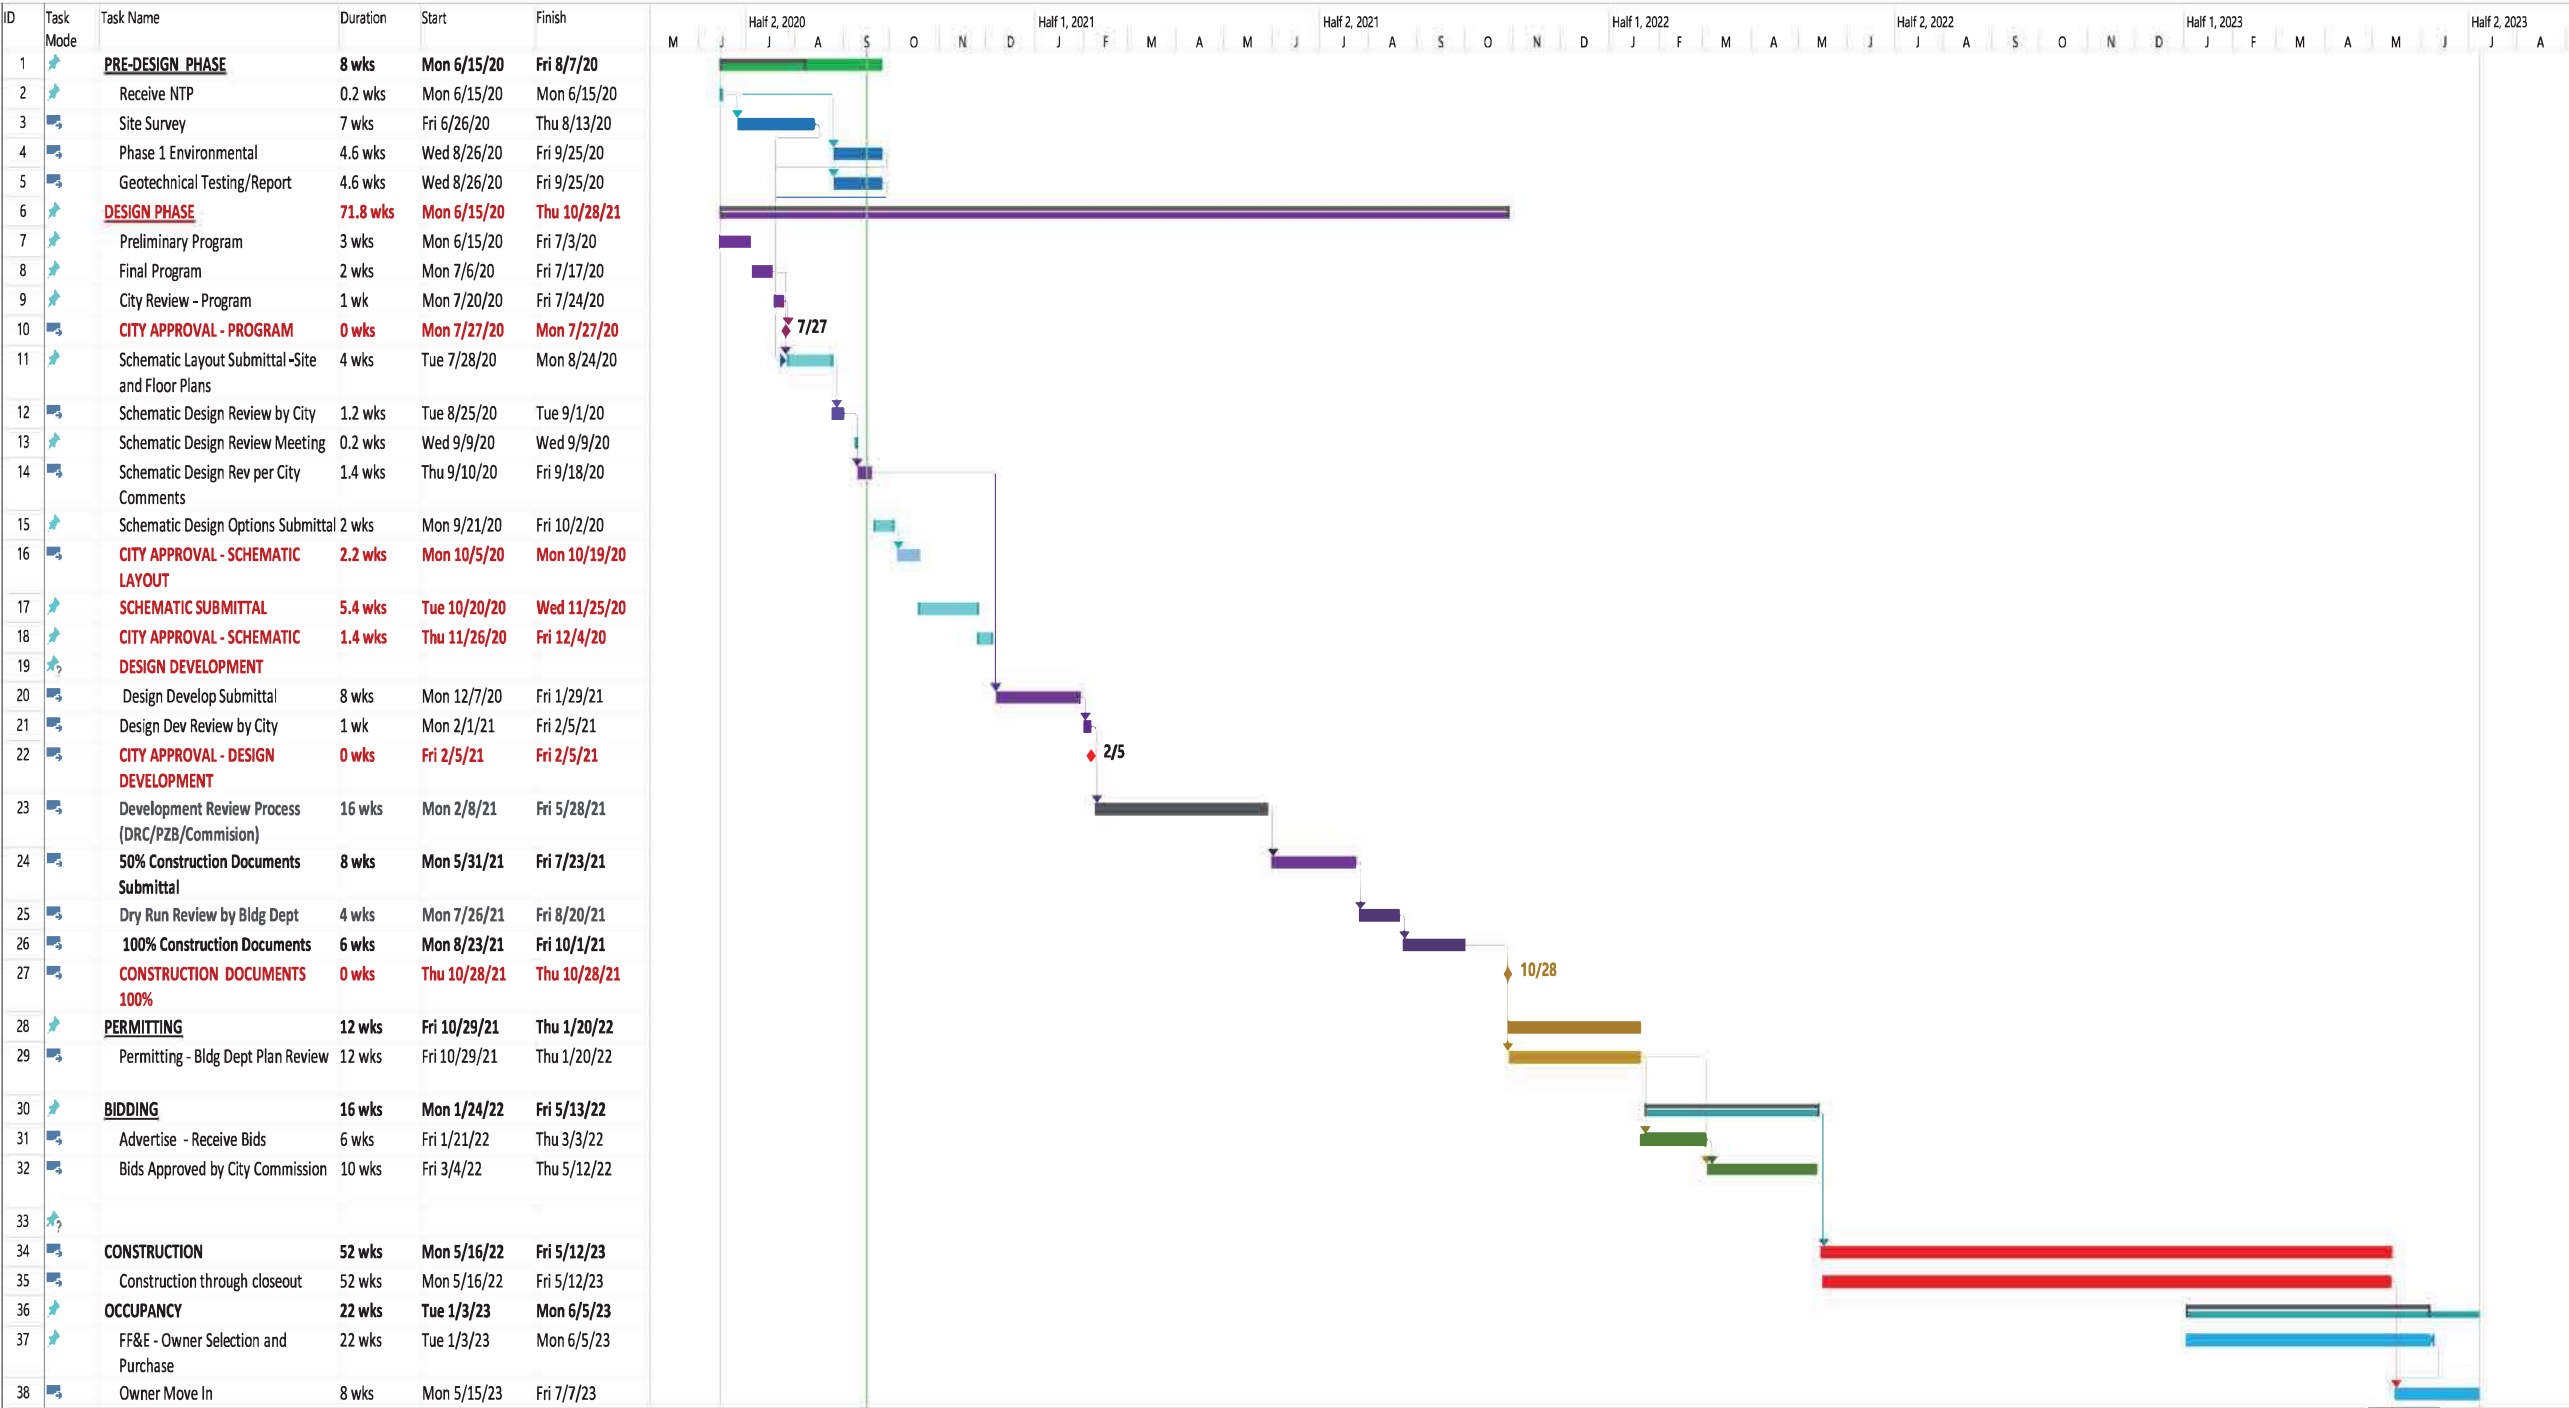



CITY OF
FORT LAUDERDALE



EXHIBIT VI: Design Schedule Temporary Fire Station #13, at 3109 Vistamar Street

