



## Memorandum

**Memorandum No: 25-012**

**Date:** February 18, 2025

**To:** Honorable Mayor, Vice Mayor, and Commissioners

**From:** Susan Grant, Acting City Manager *Susan Grant*

**Re:** **February 2025 Parks Bond Program Update**

---

On December 3, 2024, City staff provided an update on the Parks Bond signature projects at the City Commission Conference Meeting. During the presentation, the City Commission requested that staff provide more routine updates on the project status to improve transparency and community awareness.

City staff and AECOM will be providing the City Commission with a report that captures the point in time status at the beginning of each month. The report will be distributed to the City Commission around the 15<sup>th</sup> of each month.

The February 2025 report is attached for your review.

For questions, please contact Ben Rogers, Acting Assistant City Manager, at 954-828-3781 or [Brogers@fortlauderdale.gov](mailto:Brogers@fortlauderdale.gov)

Attachment: February 2025 Report

c: Anthony G. Fajardo, Assistant City Manager  
Laura Reece, Acting Assistant City Manager  
Ben Rogers, Acting Assistant City Manager  
Christopher Cooper, Acting Assistant City Manager  
D'Wayne M. Spence, Acting City Attorney  
David R. Soloman, City Clerk  
Patrick Reilly, City Auditor  
Department Directors  
CMO Managers

District 2 Parks

- |                                   |  |
|-----------------------------------|--|
| 1 Annie Beck Park                 | 10 South Middle River Park             |
| 2 Fort Lauderdale Aquatic Complex | 11 Thurgood Marshall Elementary School |
| 3 Cooley's Landing                | 12 Victoria Park                       |
| 4 Fort Lauderdale Beach Park      | 13 Virginia S. Young Elementary School |
| 5 Holiday Park                    | 14 Warfield Park                       |
| 6 Lu Deaner Park                  |  |
| 7 Peter Feldman Park              |  |
| 8 Sailboat Bend Preserve          |  |
| 9 Sistrunk Park                   |  |

District 1 Parks

- |                          |                              |                            |
|--------------------------|------------------------------|----------------------------|
| 1 Bay View Park          | 6 George English Park        | 11 Lockhart Community Park |
| 2 Beach Community Center | 7 Greenfield Park            | 12 Palm Aire Village Park  |
| 3 Dottie Mancini Park    | 8 Imperial Point Entranceway | 13 Sunrise Middle School   |
| 4 Earl Lifshy Ocean Park | 9 Jack and Harriet Kaye Park | 14 Twin Lakes North Park   |
| 5 Floranada Park         | 10 Lake Estates Linear Park  |                            |

District 3 Parks

- |                                       |
|---------------------------------------|
| 1 Bass Park                           |
| 2 Benneson Park                       |
| 3 Dillard High School                 |
| 4 Guthrie Blake Park                  |
| 5 Joseph C. Carter Park               |
| 6 Lincoln Park                        |
| 7 Mills Pond                          |
| 8 North Fork School Park              |
| 9 Osswald Park                        |
| 10 Riverland Park                     |
| 11 Rock Island Elementary School      |
| 12 Sunset Park                        |
| 13 Sweeting Park                      |
| 14 Walker Park                        |
| 15 Westwood Heights Elementary School |

District 4 Parks


- |                             |                                 |                                     |
|-----------------------------|---------------------------------|-------------------------------------|
| 1 Ann Herman Park           | 9 Floyd Hull Stadium            | 17 Sara Horn Greenway               |
| 2 Bill Keith Preserve       | 10 Fort Lauderdale Beach Park   | 18 Stephen Foster Elementary School |
| 3 Collee Hammock Park       | 11 Harbordale Elementary School | 19 Stranahan High School            |
| 4 Coontie Hatchee Park      | 12 Harbordale Park              | 20 Tarpon Cove Park                 |
| 5 Croissant Park            | 13 Hector Park                  | 21 Tarpon River Park                |
| 6 Esteree Davis Wright Park | 14 Hortt Park                   | 22 Tunnel Top Park                  |
| 7 Flamingo Park             | 15 Lauderdale Isles Landing     | 23 Virginia S. Young Park           |
| 8 Florence C. Hardy Park    | 16 Riverside Park               |                                     |

Active Park Projects Status

- Completed
- Partially Completed
- Under Construction
- Bidding & Award / Purchasing
- Design

Project Size

- Signature / Large Project
- Significant Improvements
- Small Projects

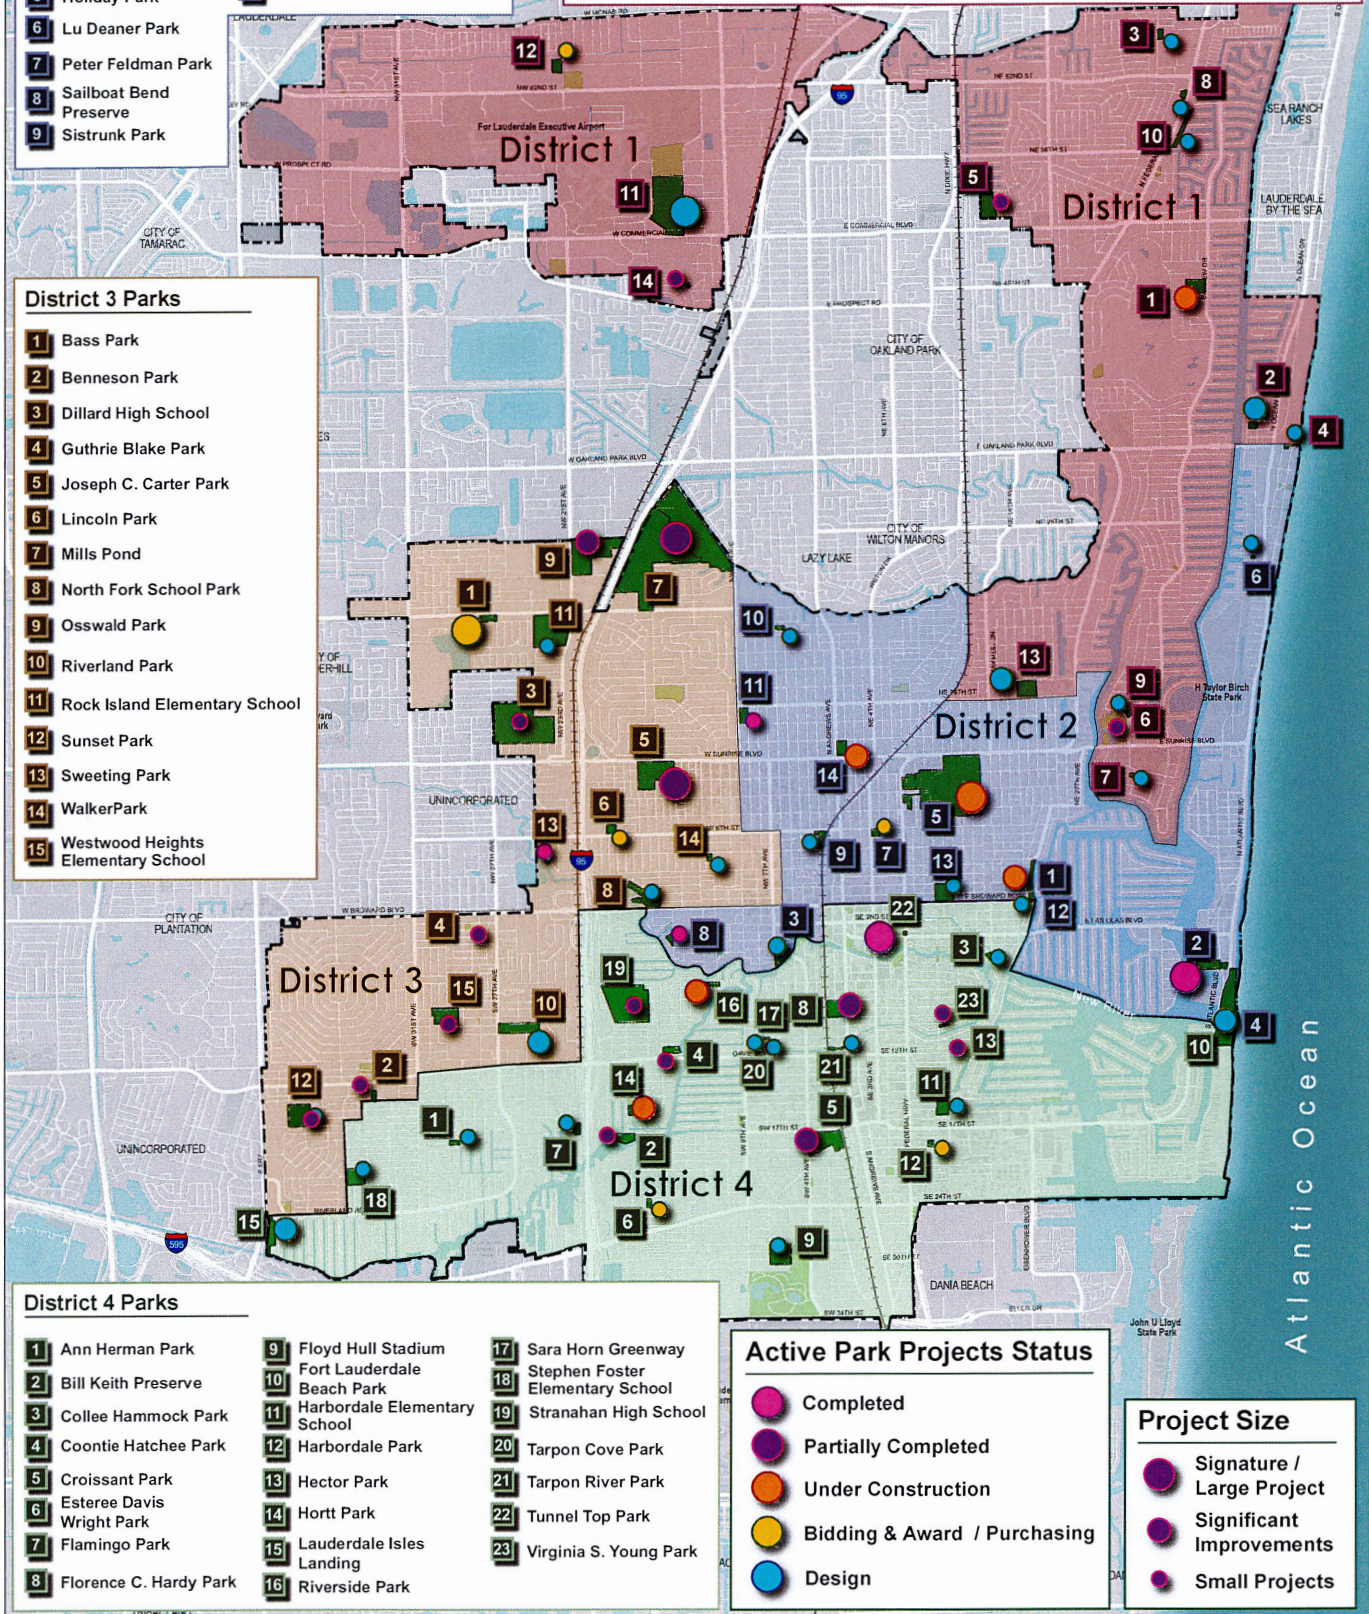

Fort Lauderdale Parks Bond - Design Task Orders(s) Status Report - 2/13/2025				
<b>DISTRICT 1</b>				
<b>1 Bayview Park</b>				
Task Orders(s)	6 & 18			
Overall Status	Construction			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	9/10/2021			
Bidding Initiated	6/21/2022			
Project Awarded	9/1/2023			
NTP for Construction Issued	12/1/2023			
<b>DRC / Permit Log</b>				
	Date Submitted	Permit Status	Date Comments Received	Date Completed
Building Permit	4/5/2023	Completed		8/8/2024
Broward County Surface Water License	2/19/2024	Completed		
<b>Action Items</b>				
	Responsibility	Date Completed		
Final sign off from Broward County Surface Water	Contractor/AECOM	In Process		
<b>Notes</b>				
Construction scheduled to be completed in February 2025.				
<b>2 Beach Community Center</b>				
Task Orders(s)	35			
Overall Status	Planning			
DRC Flag	Y			
<b>Key Milestones</b>				
Project Initiation	6/18/2024			
Public Meeting #1	4/17/2024			
Site Visit / Feasibility Assessment	8/31/2024			
<b>Action Items</b>				
	Responsibility	Date Completed		
Public Meeting #2 Scheduling	City of Fort Lauderdale	Pending		
<b>Notes</b>				
<b>3 Dottie Mancini Park</b>				
Task Orders(s)	8			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	11/30/2021			
Bid Documents Completed - Project Placed on Hold	9/1/2022			
Project Re-Initiated / Design & Cost Updates	11/12/2024			
<b>DRC / Permit Log</b>				
	Date Submitted	Permit Status	Date Comments Received	Date Completed
Building Permit		Pending Design Updates		
Broward County Surface Water License		Pending Design Updates		
<b>Action Items</b>				
	Responsibility	Date Completed		
Updated Vendor Estimate for Playground	AECOM	1/6/2025		
Updated Cost Estimates for Remaining Park	AECOM	2/6/2023		
Prioritization for Piggyback/JOC	AECOM/City of Fort Lauderdale	Pending		
<b>Notes</b>				
Project is intended to utilize piggy-back contract for playground work, and JOC for remaining items that fit within budget. Cost estimate has been updated with Vendor quote and updated quantities. Project will be subject to new requirements from Broward County. Prioritization discussion needed to determine extent of redesign for procurement.				

<b>4 Earl Lifshey Ocean Park</b>			
Task Orders(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Vendor engaged by City	1/31/2025		
Kick off meeting with Contractor through JOC	2/4/2025		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize Cost Estimates	Contractor	Pending	
<b>Notes</b>			
<b>5 Floranada Park</b>			
Task Orders(s)	N/A		
Overall Status	Partially Complete*	* Lighting improvements completed by the City. Additional improvements pending additional planning and cost evaluation	
DRC Flag	N		
<b>Key Milestones</b>			
Lighting Improvements Completed by City	2022		
Initial Site Visit for Scoping with Vendor	6/25/2024		
Playground Design Finalized	Dec-24		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Issuance of PO to vendor for playground purchase and installation.	City of Fort Lauderdale	Pending Procurement Approval of Piggyback Purchase	
<b>Notes</b>			
<b>6 George English Park</b>			
Task Orders(s)	N/A		
Overall Status	Partially Complete*	* Lighting improvements completed by the City. Additional improvements pending project approval and funding.	
DRC Flag	N		
<b>Key Milestones</b>			
Lighting Improvements Completed by City	2024		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Obtain recommendation to approve project from PRAB, and hold public hearing to adopt resolution to approve recommendation.	City of Fort Lauderdale	Pending	
<b>Notes</b>			
<b>7 Greenfield Park</b>			
Task Orders(s)	N/A		
Overall Status	Procuring Through JOC		
DRC Flag	N		
<b>Key Milestones</b>			
Site Visit for Scoping	1/23/2024		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize scope with Vendors	City of Fort Lauderdale	Pending	
<b>Notes</b>			
Project is part of a group of small projects intended to be complete using a JOC.			

<b>8 Imperial Point Entranceway</b>			
Task Orders(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Furnishings Purchased by City	1/22/2025		
Neighborhood Engagement	In process		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize Design for Improvements Based on Neighborhood Feedback	City of Fort Lauderdale	Targeting to finalize design by 2/21/2025	
<b>Notes</b>			
<b>9 Jack and Harriet Kaye Park</b>			
Task Orders(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Vendor engaged by City	1/31/2025		
Kick off meeting with Contractor through JOC	2/4/2025		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize Cost Estimates	Contractor	Pending	
<b>Notes</b>			
<b>10 Lake Estates Linear Park</b>			
Task Orders(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Neighborhood Engagement	In process		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize Design for Improvements Based on Neighborhood Feedback	City of Fort Lauderdale	Targeting to finalize design by 2/21/2025	
<b>Notes</b>			

<b>11 Lockhart Community Park</b>				
Task Order(s)	3 & 11			
Overall Status	Design/DRC Approval			
DRC Flag	Y			
<b>Key Milestones</b>				
Project Initiation (Planning)	11/30/2021			
Phase 1 ESA	9/20/2023			
Phase 2 ESA	4/18/2024			
Property Rezoning	5/7/2024			
100% CDs	11/1/2024			
Permitting	See Permit Log			
<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>
FAA	8/2/2024	Completed	8/21/2024	9/2/2024
DRC	-	Pending Resubmission #3 in February 2025	-	
DRC Submission #1	3/4/2024	-	3/26/2024	
DRC Submission #2	11/7/2024	-	1/15/2024	
DRC Submission #3		-		
Building Permit		Pending Design Updates		
Broward County Surface Water License		Pending Design Updates		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
DRC Submission #3	AECOM	Scheduled for 2/19		
DRC Final Approval	City of Fort Lauderdale	Scheduled for 3/7		
Bid Documents to City	AECOM	Scheduled for 3/31		
<b>Notes</b>				
Revisions to plans per DRC comments are underway. DRC approval received from Building, Transportation, Utilities, Airport and Police. Comments are being addressed from Landscape, Flood, Engineering, Planning and Solid Waste. Project will proceed with bid documents contingent on DRC approval.				
<b>12 Palm Aire Village Park</b>				
Task Order(s)	N/A			
Overall Status	Purchasing			
DRC Flag	N			
<b>Key Milestones</b>				
Playground Design Finalized	Dec-24			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Issuance of PO to vendor for playground purchase and installation.	City of Fort Lauderdale	Pending Procurement Approval of Piggyback Purchase		
<b>Notes</b>				

<b>13</b>	<b>Sunrise Middle School</b>			
	<b>Task Orders(s)</b>	N/A		
	<b>Overall Status</b>	Permitting		
	<b>DRC Flag</b>	N		
	<b>Key Milestones</b>			
	100% Design Plans Completed	10/1/2024		
	Bid Documents Submitted	11/26/2024		
	Permitting Set Provided t School Board of Broward County	2/5/2025		
	Stakeholder Meeting	2/13/2025		
	<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b> <b>Date Completed</b>
	Broward County School Board	2/5/2025	Pending Comments	
	Broward County Surface Water License	2/3/2025	Pending Comments	
	<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
	Finalize JOC	City of Fort Lauderdale		
	<b>Notes</b>			
	Bid documents were provided to the City on 11/26/2024. Recent communication with the City would indicate that items included in the base bid will be completed using a JOC. Permitting was initiated with Broward County 12/12/2024. Embossed seal was required on hard copies of plans. Plans were submitted on 1/27/2024. School Board notified AECOM that specs were also required (this was not previously shared). Specs were delivered on 2/4/2024. Official submission was completed on 2/5/2025. A stakeholder meeting to provide updates on the project was held on 2/13/2025.			
<b>14</b>	<b>Twin Lakes North Park</b>			
	<b>Task Orders(s)</b>	N/A		
	<b>Overall Status</b>	Partially Complete		
	<b>DRC Flag</b>	N		
	<b>Key Milestones</b>			
	Lighting Improvements are Complete	Jan-25		
	PO Issued to Playground Vendor	Jan-25		
	<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
	Obtain Target Construction Schedule for Playground Installation	Vendor	In Process	
	<b>Notes</b>			
	Playground Installation is scheduled to begin in Spring 2025.			

Fort Lauderdale Parks Bond - Design Task Orders(s) Status Report - 2/13/2025				
<b>DISTRICT 2</b>				
<b>1 Annie Beck Park</b>				
Task Orders(s)	8			
Overall Status	Pre-Construction			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	10/30/2021			
100% Construction Package - Project Placed on Hold	9/8/2022			
Bid Documents	12/12/2023			
Project Awarded	11/1/2024			
Construction Drawings to Contractor	1/14/2025			
<b>DRC / Permit Log</b>				
Building Permit	Date Submitted	Permit Status	Date Comments Received	Date Completed
Broward County Environmental Resource License	1/21/2025	Pending		
Submission #1	1/22/2024	-	4/4/2024	
Submission #2	1/17/2025			
<b>Action Items</b>				
Follow-up with Broward County	Responsibility	Date Completed		
	AECOM	Scheduled for 2/10		
<b>Notes</b>				
Project was placed on hold after CD submittal due to budget concerns. Bid documents were completed in December of 2023, with permitting for final design beginning in January 2024. Project received one bidder, and negotiations were held from June 2024 to August 2024, and design was value engineered to reduce impacts and cost. Project was again placed on hold. AECOM received notification in November of 2024 that the project would be awarded with additional funding. AECOM then proceeded with responses to permitting RAls and updated drawings for the selected contractor.				
<b>2 Aquatic Complex</b>				
Task Orders(s)	N/A			
Overall Status	Completed			
DRC Flag	N			
<b>Key Milestones</b>				
Improvements are Complete.	12/30/2022			
<b>3 Cooley's Landing</b>				
Task Orders(s)	14			
Overall Status	Design			
DRC Flag	N			
Historic Preservation Board Flag	Y			
<b>Key Milestones</b>				
Project Initiation (Planning)	7/23/2024			
Design Development	Scheduled for 2/26/2025			
<b>DRC / Permit Log</b>				
US Army Corps of Engineers	Date Submitted	Permit Status	Date Comments Received	Date Completed
Building Permit		Pending early submission February 2025		
Broward County Surface Water License		Pending submission once design phase is completed		
		Pending submission once design phase is completed		
<b>Action Items</b>				
Design Development Submission	Responsibility	Date Completed		
Grant Information (Submission deadlines and requirements, timelines, etc.)	AECOM	Ongoing		
Exploration for additional funding sources	City of Fort Lauderdale	Pending		
<b>Notes</b>				
Initial site visit was completed 8/12/2024 followed by cost validation exercises submitted to the City in September 2024 that determined the project would be overbudget. City provided directive to change bidding methodology for the park and requested a change order be prepared to issue a Design Criteria Package in lieu of the traditional design-bid-build process. City provided final directive in November 2024 to revert to the original scope of work detailed in the initial task order. Design development restarted and currently following agreed-upon schedule.				

<b>4 Fort Lauderdale Beach Park</b>				
Task Order(s)	23			
Overall Status	Planning			
DRC Flag	N			
<b>Key Milestones</b>				
Permitting Investigation/Feasibility Assessment	1/16/2025			
<b>Action Items</b>				
Task Order Development	Responsibility	AECOM	Date Completed	Pending
<b>Notes</b>				
Initial investigation for feasibility of improvements. Task Order development is underway.				
<b>5 Holiday Park</b>				
Task Order(s)	5, 13, & 43			
Overall Status	Design/ Construction			
DRC Flag	Y			
<b>Key Milestones</b>				
Project Initiation (Planning)	3/4/2021			
Bid Documents for Full Project	6/21/2024			
Direction to Split Bid Packages	7/30/2024			
DRC Approval	9/24/2024			
JETC Bid Document Submittal	8/21/2024			
Remaining Park Bid Document Submittal	11/26/2024			
JETC Bids Received	10/22/2024			
JETC Moved Towards Award	11/18/2024			
JETC Award Approved	12/3/2024			
JETC Pre-construction Initiated	12/17/2024			
JETC Construction NTP	Pending City Issuance after Approval of Early Start Permit			
<b>DRC / Permit Log</b>				
Building Permit (JETC)	Date Submitted	9/16/2024	Permit Status	Contractor Ongoing
Building Permit (Remaining Park excluding Restroom and Splash pad)			Date Comments Received	11/25/2024
Broward County Surface Water License JETC			Date Completed	
Submission #1	11/20/2024	-	12/11/2024	
Submission #2	12/31/2024	-	1/22/025	
Submission #3	1/28/2025	-		
<b>Action Items</b>				
RFIs/Submittals	Responsibility	AECOM	Date Completed	Ongoing
Surface Water Permit	AECOM			Pending Submission February
Solicitation for Remaining Park	City of Fort Lauderdale			Pending
<b>Notes</b>				
Design for the full park was initiated in June of 2023. As the project has progressed, the scope of the JETC has expanded. After coordination with the Panthers and exploration of different alternatives, pickleball was moved to a later phase. Bid documents for the full park (including JETC) were provided on 6/21/2024. AECOM was then directed to split this work to include a package for the JETC and a package for the remainder of the park (excluding pickleball). The JETC bid package was submitted on 8/21/2024. Bids were received on 10/22/2024. The City indicated that these bids may be rejected due to compliance issues. AECOM was then notified of intent to award on 11/18/2024. The JETC project was awarded to Shiff Construction on 12/3/2024. Due to budget concerns after the JETC bids, the remaining park package was modified to move the splash pad and restroom until a later phase. The remaining park bid package was submitted on 12/3/2024. AECOM continues to work with Shiff and the City on permitting, RFIs and Submittals for the JETC project. Shiff received approval for an Early Start Permit on 2/4/2025.				
<b>6 Lu Deaner Park</b>				
Task Order(s)	N/A			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Vendor engaged by City	1/31/2025			
Kick off meeting with Contractor through JOC	2/4/2025			
<b>Action Items</b>				
Finalize Cost Estimates	Responsibility	Contractor	Date Completed	Pending
<b>Notes</b>				

<b>7 Peter Feldman Park</b>			
Task Orders(s)	N/A		
Overall Status	Purchasing		
DRC Flag	N		
<b>Key Milestones</b>			
Initial Site Visit for Scoping with Vendor	6/25/2024		
Playground Design Finalized	Dec-24		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Issuance of PO to vendor for playground purchase and installation.	City of Fort Lauderdale	Pending Procurement Approval of Piggyback Purchase	
<b>Notes</b>			
<b>8 Sailboat Bend Preserve Park</b>			
Task Orders(s)	N/A		
Overall Status	Complete		
DRC Flag	N		
<b>Key Milestones</b>			
Improvements are Complete.	2024		
<b>9 Sistrunk Park</b>			
Task Orders(s)	N/A		
Overall Status	Procuring Through JOC		
DRC Flag	N		
<b>Key Milestones</b>			
Survey Completed	12/21/2023		
Site Visit for Scoping	1/23/2024		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize scope and pricing with Vendors	City of Fort Lauderdale	Coordination is Ongoing	
<b>Notes</b>			
Project is part of a group of small projects intended to be complete using a JOC.			
<b>10 South Middle River Park</b>			
Task Orders(s)	N/A		
Overall Status	Planning		
DRC Flag	N		
<b>Key Milestones</b>			
Vendor engaged by City	1/31/2025		
Kick off meeting with Contractor through JOC	2/4/2025		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize Cost Estimates	Contractor	Pending	
<b>Notes</b>			
<b>11 Thurgood Marshall Elementary</b>			
Task Orders(s)	27		
Overall Status	Partially Complete*		* Court Renovations completed by the City. Additional improvements pending approval by the School Board.
DRC Flag	N		
<b>Key Milestones</b>			
Court Renovations	5/1/2024		
Program Plans and Cost Validation	8/21/2023		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Obtain School Board Approval for Remainder of Improvements	City of Fort Lauderdale	Coordination is Ongoing	
<b>Notes</b>			
Pending direction on improvements.			

<b>12 Victoria Park</b>				
Task Orders(s)	N/A			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Vendor engaged by City	10/29/2024			
Site Visit for Scoping with Vendor	11/4/2024			
Site Survey Initiated	1/30/2025			
<b>Action Items</b>				
Finalize Conceptual Playground Design	Playground Vendor	Target Completion by 2/14/2025		
Complete Survey	City of Fort Lauderdale	Target Completion by 2/28/2025		
<b>Notes</b>				
<b>13 Virginia S. Young Elementary School</b>				
Task Orders(s)	27			
Overall Status	Planning			
DRC Flag	N			
<b>Key Milestones</b>				
Program Plans and Cost Validation	8/21/2023			
<b>Action Items</b>				
Obtain School Board Approval for Remainder of Improvements	City of Fort Lauderdale	Coordination is Ongoing		
<b>Notes</b>				
Pending direction on improvements.				
<b>14 Warfield Park</b>				
Task Orders(s)	8			
Overall Status	Construction			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	11/30/2021			
Bidding Initiated	1/16/2023			
Project Awarded	8/1/2024			
NTP for Construction Issued	1/29/2025			
<b>DRC / Permit Log</b>				
Building Permit	Date Submitted	Permit Status	Date Comments Received	Date Completed
Building Permit	4/5/2023	Completed		
Broward County Surface Water License	03/09/2023	Completed		
<b>Action Items</b>				
RFI/Submittals Responses	AECOM	Ongoing		
<b>Notes</b>				
Submittal review began mid January 2025. Contractor in process of addressing owner/contractor coordinated comments for the building department.				

Fort Lauderdale Parks Bond - Design Task Orders(s) Status Report				
<b>DISTRICT 3</b>				
<b>1 Bass Park</b>				
Task Orders(s)	7			
Overall Status	Award of Contract			
DRC Flag	Y			
<b>Key Milestones</b>				
Project Initiation (Planning)	9/13/2021			
Construction Documents	5/22/2023			
City Coordination Period (DRC comment approval assistance)	5/23/2023-11/3/2023			
Bid Documents and Bidding Assistance Initiated	4/25/2024			
DRC Approval	8/9/2024			
Pre- Bid Conference	11/20/2024			
Commission Approval	-		Pending March 2025	
Award of Contract	-		Pending March - April 2025	
<b>DRC / Permit Log</b>				
	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>
Building Permit	12/22/2023	Ongoing		
Broward County Surface Water License	07/26/2023	Ongoing		
<b>Action Items</b>				
	<b>Responsibility</b>	<b>Date Completed</b>		
Commission Approval	City of Fort Lauderdale	Pending		
Award of Contract timeline	City of Fort Lauderdale	Pending		
CEI Task Order Redevelopment	AECOM	Ongoing		
<b>Notes</b>				
Bids received on January 6, 2025 and showed to be overbudget. After evaluation of bids, AECOM and City agreed that no deductions could be made so the recommendation was made to award the bid to the lowest bidder, requiring commission approval- potentially in March or April 2025. City of Fort Lauderdale is looking to award the full scope of work including the alternates. Building Department permitting technical revisions addressed with owner/contractor comments pending.				
<b>2 Benenson Park</b>				
Task Orders(s)	N/A			
Overall Status	Partially Complete*		* Basketball court renovations completed by the City. Additional improvements pending additional planning and cost evaluation.	
DRC Flag	N			
<b>Key Milestones</b>				
Survey Completed	10/19/2023			
Basketball Court Renovations Completed	Jan-25			
<b>Action Items</b>				
	<b>Responsibility</b>	<b>Date Completed</b>		
Prioritization of the Remainder of the Scope of Improvements	City of Fort Lauderdale	In Process		
<b>Notes</b>				
<b>3 Dillard High School</b>				
Task Orders(s)	27			
Overall Status	Completed			
DRC Flag	N			
<b>Key Milestones</b>				
Improvements are Complete.	2024			

<b>4 Guthrie Blake Park</b>				
Task Orders(s)	N/A			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Survey Completed	12/21/2023			
Playground Vendor Engaged by City	10/22/2024			
Site Visit for Scoping with Vendor	10/24/2024			
Designs Provided by Vendor for Neighborhood Approval	12/9/2024			
<b>Action Items</b>				
Obtain Final Approval from Neighborhood	City of Fort Lauderdale	Ongoing		
<b>Notes</b>				
<b>5 Joseph C. Carter Park</b>				
Task Orders(s)	4 & 12			
Overall Status	Design			
DRC Flag	Y			
<b>Key Milestones</b>				
Project Initiation (Planning)	11/30/2021			
Conceptual Design	10/25/2022			
Schematic Design	1/25/2023			
Design Development - Project Placed on Hold	7/28/2023			
<b>DRC / Permit Log</b>				
DRC Submission #1	8/11/2023	Pending Design Updates		
Building Permit		Pending Design Updates		
Broward County Surface Water License		Pending Design Updates		
<b>Action Items</b>				
City Design Directive	City of Fort Lauderdale	Pending		
Existing Gymnasium FEMA Appraisal	City of Fort Lauderdale	Pending		
<b>Notes</b>				
Project was placed on hold after the deliverable of the Design Development Package and DRC submittal as the City of Fort Lauderdale pursued additional funding for the project. City notified AECOM in November 2024 that the City would like to explore a different design approach from the current approved concept plans which would require the renovation of the existing gymnasium, bring up flood plain concerns of feasibility. City and AECOM met with FTL's Building Department Flood plain manager in January 2025 to discuss next steps. City to appraise existing gymnasium and provide additional directives.				
<b>6 Lincoln Park</b>				
Task Orders(s)	N/A			
Overall Status	Procuring Through JOC			
DRC Flag	N			
<b>Key Milestones</b>				
Survey Completed	12/5/2023			
Site Visit for Scoping	1/23/2024			
<b>Action Items</b>				
Finalize scope and pricing with Vendors	City of Fort Lauderdale			
<b>Notes</b>				
Project is part of a group of small projects intended to be completed using a JOC.				

<b>7</b>	<b>Mills Pond Park</b>			
	<b>Task Order(s)</b>	<b>6 &amp; 40</b>		
	<b>Overall Status</b>	<b>Design</b>		
	<b>DRC Flag</b>	<b>Y</b>		
	<b>Key Milestones</b>			
	Project Initiation (Planning)	9/13/2021		
	Construction Documents	8/23/2022		
	Permitting Initiation/DRC Coordination	8/24/2022-2/2/2024		
	Bid Documents and Bidding Assistance Initiated	3/7/2024		
	Direction to Redesign and Split Packages	7/25/2024		
	Reissuance of Bid Documents (Restroom)	10/11/2024		
	Bid Received for Restroom	1/28/2025		
	<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>
	Building Permit			
	Permit Submittal #1 for the entire park	2/2/2024	Revised per DSD Office Request	
	Permit Submittal #2 Split as Requested by DSD office	4/8/2024	-	5/1/2024
	Permit Submittal #3 for Restroom Building Package	11/13/2024	-	1/6/2025
	Permit Submittal #4 for Restroom Building Package		Pending Resubmission February 2025	
	Broward County Surface Water License (Full Park)	11/3/2022	Cancelled	
	Broward County Surface Water License (Restroom)	11/7/2024	Ongoing	11/25/2024
	<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
	Permit Resubmittal for the Restroom Building	AECOM	Ongoing	
	CEI Task Order Redevelopment	AECOM	Ongoing	
	Award of Contract for Restroom	City of Fort Lauderdale	Ongoing	
	Updated Design for Playground (Pending LSI update)	AECOM	Ongoing	
	<b>Notes</b>			
	Design for the full park was initiated in September of 2021. Project progressed with the design of the full park up through construction documents until 8/23/2022. Surface Water permit was submitted to Broward County on 11/3/2022. Initial Surface Water Permit was cancelled due to unresolved payment from previous 2018 permit. AECOM coordinated with the DRC through multiple rounds of submissions and revisions through 2/2/2024. Once DRC and Broward Permits were resolved, and Bid documents were submitted on 3/7/2023. Bid documents included restroom building and site work for the rest of the park. Bids came pack significantly over budget. AECOM was directed to proceed with bid documents restroom building as a separate package. Redesign was required due to updates to COFL building FEE requirements, and Broward County permitting requirements. Bid documents for the restroom building were submitted on 10/11/2024. Remaining improvements have been coordinated with COFL pending results of restroom bidding and permitting comments from Broward County. After coordination with COFL, it was determined that the playground improvements were to be prioritized. Playground improvement package is now pending updates form the vendor to comply with Broward County requirements.			
<b>8</b>	<b>North Fork School Park</b>			
	<b>Task Order(s)</b>	<b>27</b>		
	<b>Overall Status</b>	<b>Planning</b>		
	<b>DRC Flag</b>	<b>N</b>		
	<b>Key Milestones</b>			
	Program Plans and Cost Validation	8/21/2023		
	<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
	Obtain School Board Approval for Remainder of Improvements	City of Fort Lauderdale	Coordination is Ongoing	
	<b>Notes</b>			
	Pending direction on improvements.			

<b>9 Osswald Park</b>				
<b>Task Orders(s)</b>	<b>17</b>			
<b>Overall Status</b>	<b>Design</b>			
<b>DRC Flag</b>	<b>N</b>			
<b>Key Milestones</b>				
Project Initiation	6/26/2023			
60% Design Development Package - Project Placed on Hold	3/20/2024			
100% Construction Documents - Project Placed on Hold	10/4/2024			
Project Reinitiated	1/9/2025			
Redesign - 100% Construction Documents			Pending change order development	
<b>DRC / Permit Log</b>				
<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>
Building Permit		Pending submission once design phase is completed		
Broward County Surface Water License		Pending submission once design phase is completed		
<b>Action Items</b>				
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Change Order Development	AECOM	Ongoing		
<b>Notes</b>				
In response to significant projected budgetary shortfalls, The City notified AECOM on 11/01/24 that the project will be temporarily placed on hold following the deliverable of 100% CD package. City advised AECOM that Osswald Park may move forward to bid document preparation phase on 1/9/2025 pending the evaluation of City directive, which removes the interactive water fountain from the scope of work. The impact evaluation determined that redesign of playground and utilities within the impacted area will be required. AECOM to prepare change order for the plan revisions for an expedited resubmission of CDs.				
<b>10 Riverland Park</b>				
<b>Task Orders(s)</b>	<b>21</b>			
<b>Overall Status</b>	<b>Planning</b>			
<b>DRC Flag</b>	<b>N</b>			
<b>Key Milestones</b>				
Splash Pad Renovation Proposal Obtained	11/25/2024			
Latest Playground Design & Proposal Obtained	1/27/2025			
<b>Action Items</b>				
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Provide direction for task order development	City of Fort Lauderdale	Scheduled for 2/14/2025		
<b>Notes</b>				
Initial investigation for feasibility of improvements. Task Order development is underway.				
<b>11 Rock Island Elementary School</b>				
<b>Task Orders(s)</b>	<b>27</b>			
<b>Overall Status</b>	<b>Planning</b>			
<b>DRC Flag</b>	<b>N</b>			
<b>Key Milestones</b>				
Program Plans and Cost Validation	8/21/2023			
<b>Action Items</b>				
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Obtain School Board Approval for Remainder of	City of Fort Lauderdale	Coordination is Ongoing		
<b>Notes</b>				
Pending direction on improvements.				

<b>12 Sunset Park</b>			
Task Orders(s)	27		
Overall Status	Partially Complete*	* Lighting Improvements completed by the City. Additional improvements pending approval by the School Board.	
DRC Flag	N		
<b>Key Milestones</b>			
Lighting Improvements Completed by City	2023		
Program Plans and Cost Validation	8/21/2023		
<b>Action Items</b>			
	<b>Responsibility</b>	<b>Date Completed</b>	
Obtain School Board Approval for Remainder of Improvements	City of Fort Lauderdale	Coordination is Ongoing	
<b>Notes</b>			
Pending direction on improvements.			
<b>13 Sweeting Park</b>			
Task Orders(s)	N/A		
Overall Status	Complete		
DRC Flag	N		
<b>Key Milestones</b>			
Improvements are Complete.	2024		
<b>14 Walker Park</b>			
Task Orders(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Vendor engaged by City	12/5/2024		
Site Visit for Scoping with Vendor	12/10/2024		
<b>Action Items</b>			
	<b>Responsibility</b>	<b>Date Completed</b>	
Finalize Conceptual Playground Design	Playground Vendor	In Process	
<b>Notes</b>			
<b>15 Westwood Heights Elementary School</b>			
Task Orders(s)	27		
Overall Status	Partially Complete*	* Court Renovations completed by the City. Additional improvements pending approval by the School Board.	
DRC Flag	N		
<b>Key Milestones</b>			
Court Renovations completed by the City.	2024		
Program Plans and Cost Validation	8/21/2023		
<b>Action Items</b>			
	<b>Responsibility</b>	<b>Date Completed</b>	
Obtain School Board Approval for Remainder of Improvements	City of Fort Lauderdale	Coordination is Ongoing	
<b>Notes</b>			
Pending direction on improvements.			

Fort Lauderdale Parks Bond - Design Task Orders(s) Status Report			
DISTRICT 4			
<b>1 Ann Herman Park</b>			
Task Orders(s)	N/A		
Overall Status	Pre-Construction		
DRC Flag	N		
Key Milestones			
PO Issued to Vendor			
<b>Action Items</b>			
Obtain Target Construction Schedule	Responsibility	Date Completed	
	Playground Vendor	In Process	
<b>Notes</b>			
Design for the playground replacement was originally completed in October 2022. After the designed was approved by the neighborhood, the purchasing process was initiated. In a response to delays attributed to purchasing limitations. Staff identified another piggyback contract in July 2024 to proceed with the work. A PO was issued to the vendor for the new playground and outdoor fitness equipment. The installation is currently scheduled to begin in Spring 2025.			
<b>2 Bill Keith Preserve</b>			
Task Orders(s)	N/A		
Overall Status	Partially Complete*		
DRC Flag	N		
Key Milestones			
Boardwalk Complete	2024		
<b>Action Items</b>			
Perform the remainder of the improvements	Responsibility	Date Completed	
	City of Fort Lauderdale	Work is in process.	
<b>Notes</b>			
*Boardwalk completed by the City. Additional improvements in design and cost evaluation phase.			
<b>3 Colee Hammock Park</b>			
Task Orders(s)	N/A		
Overall Status	Procurement Through JOC		
DRC Flag	N		
Key Milestones			
Site Visit for Scoping	1/23/2024		
<b>Action Items</b>			
Finalize scope and pricing with Vendors	Responsibility	Date Completed	
	City of Fort Lauderdale	Coordination is Ongoing	
<b>Notes</b>			
Project is part of a group of small projects intended to be complete using a JOC.			
<b>4 Coontie Hatchee Park</b>			
Task Orders(s)	N/A		
Overall Status	Partially Complete*		
DRC Flag	N		
Key Milestones			
Playground Improvements	2021		
Final Site Evaluation Completed	2/6/2025		
<b>Action Items</b>			
Purchase materials/equipment and schedule installation	Responsibility	Date Completed	
	City of Fort Lauderdale	In Process	
<b>Notes</b>			
* Playground Improvements have been completed by the City. Additional improvements in design and cost evaluation phase.			

<b>5 Croissant Park</b>				
Task Orders(s)	19			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	6/26/2024			
60% Design Development Package - Project Placed on Hold	3/20/2024			
Project Reinitiated	1/9/2025			
100% Construction Document Package	Scheduled for 4/11/2025			
<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>
Building Permit		Pending submission once design phase is completed		
Broward County Surface Water License		Pending submission once design phase is completed		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Revised Construction Drawings	AECOM	Ongoing		
<b>Notes</b>				
In response to significant projected budgetary shortfalls, City notified AECOM that the project will be temporarily on hold following the deliverable of 60% Design Development package. City advised AECOM that Croissant Park may move forward to construction document preparation phase on 1/9/2025 pending the evaluation of City directive, which removes the interactive water fountain from the scope of work. The impact evaluation determined that no redesign would be required. AECOM is currently working on the CD package.				
<b>6 Esterre Davis Wright Park</b>				
Task Orders(s)	N/A			
Overall Status	Purchasing			
DRC Flag	N			
<b>Key Milestones</b>				
Initial Site Visit for Scoping with Vendor	6/25/2024			
Playground & Fitness Station Design Finalized	Dec-24			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Issuance of PO to vendor for playground purchase and installation.	City of Fort Lauderdale	Pending Procurement Approval of Piggyback Purchase		
<b>Notes</b>				
<b>7 Flamingo Park</b>				
Task Orders(s)	N/A			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Initial Site Visit for Scoping with Vendor	6/25/2024			
First Conceptual Design for Playground, Fitness Station and Loop Trail Received	9/19/2024			
Latest Iteration of Design for Playground, Fitness Station and Loop Trail Received	12/1/2024			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Revise plans and proposal to fall within purchasing threshold for piggyback purchases.	Playground Vendor	In Process		
<b>Notes</b>				

<b>8 Florence C. Hardy Park</b>				
<b>Task Orders(s)</b>	<b>6 &amp; 39</b>			
<b>Overall Status</b>	<b>Design</b>			
<b>DRC Flag</b>	N			
<b>Key Milestones</b>				
Project Initiation	9/10/2021			
Bid Documents Packages for Playground and Site (Phase 1)	9/12/2023			
Phase 1 Awarded	9/17/2024			
Construction Initiation for Phase 1	1/29/2025			
TO 39 Turf Field (Phase ) Initiated	12/3/2024			
Revised Construction Drawings for Phase 2	Scheduled for 2/14/2025			
<b>DRC / Permit Log</b>				
<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>	
Building Permit	4/29/2024	Approved pending payment of fees		
Broward County Surface Water License Phase 1	9/12/2024	Completed		
Broward County Surface Water License Phase 2	1/29/2025	Ongoing		
<b>Action Items</b>				
<b>Responsibility</b>	<b>Date Completed</b>			
Revised Construction Drawings	AECOM	Pending		
Building Permit fees payment for issuance of approval	Contractor	Pending		
<b>Notes</b>				
Phase 1 of project includes Playground installation performed through piggy-back contract. Additional site work completed under contract awarded to low bidder. Turf field (Phase 2) was removed from original scope after the CD deliverable. Phase 2 redesign underway after determination of grading and drainage updates per Broward County revised groundwater elevations issued in June 2024.				
<b>9 Floyd Hull Stadium</b>				
<b>Task Orders(s)</b>	<b>28</b>			
<b>Overall Status</b>	<b>Planning</b>			
<b>DRC Flag</b>	Y			
<b>Key Milestones</b>				
Project Initiation	7/12/2023			
Public Meeting #1	4/18/2024			
Site Visit / Feasibility Assessment	8/9/2024			
Final Concept & City Review	8/20/2024			
Stakeholder Meeting	9/10/2024			
<b>Action Items</b>				
<b>Responsibility</b>	<b>Date Completed</b>			
Public Meeting #2 Scheduling	City of Fort Lauderdale	Pending		
<b>Notes</b>				
City staff and Commissioner working to schedule meeting with neighborhood association.				
<b>10 Fort Lauderdale Beach Park</b>				
<b>Task Orders(s)</b>	<b>23</b>			
<b>Overall Status</b>	<b>Planning</b>			
<b>DRC Flag</b>	N			
<b>Key Milestones</b>				
Permitting Investigation/Feasibility Assessment	1/16/2025			
<b>Action Items</b>				
<b>Responsibility</b>	<b>Date Completed</b>			
Task Order Development	AECOM			
<b>Notes</b>				
Initial investigation for feasibility of improvements. Task Order development is underway.				

<b>11 Harbordale Elementary School</b>				
Task Orders(s)	27			
Overall Status	Planning			
DRC Flag	N			
<b>Key Milestones</b>				
Program Plans and Cost Validation	8/21/2023			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Obtain School Board Approval for Remainder of Improvements	City of Fort Lauderdale	Coordination is Ongoing		
<b>Notes</b>				
Pending direction on improvements.				
<b>12 Harbordale Park</b>				
Task Orders(s)	N/A			
Overall Status	Purchasing			
DRC Flag	N			
<b>Key Milestones</b>				
Initial Site Visit for Scoping with Vendor	6/25/2024			
Playground & Fitness Station Design Finalized	Dec-24			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Issuance of PO to vendor for playground purchase and installation.	City of Fort Lauderdale	Pending Procurement Approval of Piggyback Purchase		
<b>Notes</b>				
<b>13 Hector Park</b>				
Task Orders(s)	N/A			
Overall Status	Complete			
DRC Flag	N			
<b>Key Milestones</b>				
Improvements are Complete.	2023			
<b>14 Hortt Park</b>				
Task Orders(s)	7 & 18			
Overall Status	Construction			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	9/10/2021			
Bidding Initiated	6/21/2022			
Project Awarded	9/1/2023			
Construction Initiated	12/1/2023			
<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>
Building Permit	4/5/2023	Completed		5/10/2024
Broward County Surface Water License		Completed		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Final sign off from Broward County Surface Water	Contractor/AECOM	In Process.		
<b>Notes</b>				
Construction scheduled to be completed in February 2025.				

<b>15 Lauderdale Isles Landing</b>				
Task Orders(s)	38			
Overall Status	Design			
DRC Flag	Y			
<b>Key Milestones</b>				
Project Initiation	10/16/2024			
Site Visit	6/21/2022			
Concept Alternatives	1/24/2025			
Stakeholder Meeting #1	2/5/2025			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Stakeholder Meeting #1	AECOM/City of Fort Lauderdale	2/5/2025		
Attend Neighborhood Association Meeting	AECOM/City of Fort Lauderdale	Scheduled for March, 2025		
<b>Notes</b>				
<b>16 Riverside Park</b>				
Task Orders(s)	7 & 18			
Overall Status	Construction			
DRC Flag	N			
<b>Key Milestones</b>				
Project Initiation	9/10/2021			
Bidding Initiated	6/21/2022			
Project Awarded	9/1/2023			
NTP for Construction Issued	12/1/2023			
<b>DRC / Permit Log</b>	<b>Date Submitted</b>	<b>Permit Status</b>	<b>Date Comments Received</b>	<b>Date Completed</b>
Building Permit	4/5/2023	Completed		5/10/2024
Broward County Surface Water License		Completed		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
<b>Notes</b>				
Construction scheduled to be completed in February 2025.				
<b>17 Sara Horn Greenway</b>				
Task Orders(s)	N/A			
Overall Status	Design			
DRC Flag	N			
<b>Key Milestones</b>				
Final Site Evaluation Completed	2/6/2025			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Purchase materials/equipment and schedule installation	City of Fort Lauderdale	In Process		
<b>Notes</b>				
<b>18 Stephen Foster Elementary</b>				
Task Orders(s)	27			
Overall Status	Planning			
DRC Flag	N			
<b>Key Milestones</b>				
Program Plans and Cost Validation	8/21/2023			
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>		
Obtain School Board Approval for Improvements	City of Fort Lauderdale	Coordination is Ongoing		
<b>Notes</b>				
Pending direction on improvements.				

<b>19 Stranahan High School</b>			
Task Order(s)	27		
Overall Status	Partially Complete*	* Tennis Court renovation and pickleball conversion is complete. Remainder of improvements are pending school board approval.	
DRC Flag	N		
<b>Key Milestones</b>			
Program Plans and Cost Validation	8/21/2023		
Tennis Court renovation and pickleball conversion is complete.	2024		
Latest meeting held with new school principal	1/8/2025		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Obtain School Board Approval for the Remainder of the Improvements	City of Fort Lauderdale	Coordination is Ongoing	
<b>Notes</b>			
<b>20 Tarpon Cove Park</b>			
Task Order(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Final Site Evaluation Completed	2/6/2025		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Purchase materials/equipment and schedule installation	City of Fort Lauderdale	In Process	
<b>Notes</b>			
<b>21 Tarpon River Park</b>			
Task Order(s)	N/A		
Overall Status	Design		
DRC Flag	N		
<b>Key Milestones</b>			
Final Site Evaluation Completed	2/6/2025		
<b>Action Items</b>	<b>Responsibility</b>	<b>Date Completed</b>	
Purchase materials/equipment and schedule installation	City of Fort Lauderdale	In Process	
<b>Notes</b>			
<b>22 Tunnel Top Park</b>			
Task Order(s)	N/A		
Overall Status	Complete		
DRC Flag	N		
<b>Key Milestones</b>			
Improvements are Complete.	2024		
<b>23 Virginia S. Young Park</b>			
Task Order(s)	N/A		
Overall Status	Complete		
DRC Flag	N		
<b>Key Milestones</b>			
Improvements are Complete.	2021		
