


Work on the Stormwater/Resilience Master Plan continues to progress throughout vulnerable neighborhoods in the City. Updated project progress is provided below. Work continues on planning efforts associated with the Tranche 2 neighborhoods, including updates to the City’s existing stormwater model allowing simulation of current and future conditions to inform stormwater improvements.

Neighborhood	Project Status
1a Edgewood *	Construction substantially complete
1b Osceola Creek Dredging (Edgewood) *	Construction substantially complete
2a River Oaks (Underground Utilities) *	Construction substantially complete
2b River Oaks (Pump Stations)	In Construction
3 Durrs *	Stormwater infrastructure installation is completed. Existing infrastructure maintenance and restoration activities are ongoing.
4 Dorsey-Riverbend	In Construction
5 Progresso Village	Design being updated; Bidding Fourth Quarter 2024
6 Southeast Isles	Design being updated; Bidding Third Quarter 2025
6a Southeast Isles Seawalls Replacement	Construction substantially complete
7 Victoria Park	Design being updated; Bidding First Quarter 2025
8 Melrose Manors/ Riverland Civic	Estimated design completion Fourth Quarter 2025

* Construction ahead of schedule

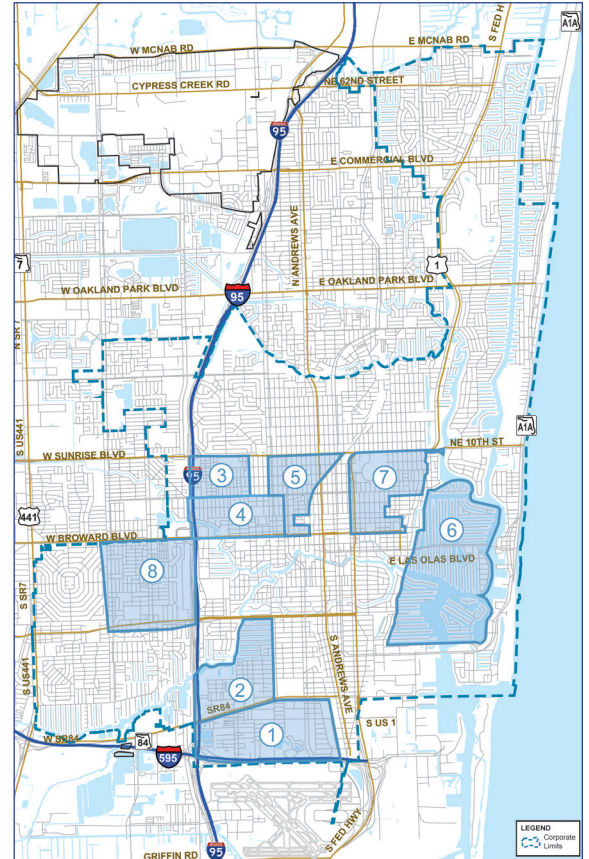

The Dorsey-Riverbend Neighborhood Stormwater Improvements project commenced construction.

The project includes a stormwater gravity system with pipes ranging from 18 to 66 inches, swale rehabilitation, exfiltration trenches, a stormwater pump station, and a new outfall at the New River. These infrastructure improvements will connect to the Durrs Neighborhood project to the north, allowing both neighborhoods to realize the full benefits of the stormwater system.

Construction completion is anticipated in 2026.

